7.2 Water Quality Monitoring

GPCB has been actively involved in the systematic monitoring of water quality across the state through various Central and State-sponsored programs. These efforts aim to assess the impact of anthropogenic activities on water bodies, identify pollution sources, and support environmental planning and regulatory interventions. The following table presents the number of water monitoring stations operated by GPCB

GEMS	MINARS	Annual status	Well water	Major cities	Bio monitoring	Coastal monitoring
9	132	199	104	92	31	56

7.2.1 Global Environmental Monitoring System (GEMS) Project

GPCB continues its proactive role in environmental monitoring through its participation in the Global Environmental Monitoring System (GEMS) project which is an initiative of CPCB that has been active in Gujarat since 1980.


The project focuses on assessing water quality of major rivers and groundwater sources across the state. GPCB operates a total of 9 monitoring stations under the GEMS project:

- 7 Surface Water Stations: Monitoring water quality in key rivers—Narmada, Sabarmati, Mahi and Tapi
- 2 Groundwater Stations: Monitoring borewell water in Ahmedabad and Vadodara

Location wise annual average results of water monitoring carried out under the GEMS project of year 2024-25 is given in **Annexure – 19.**

Data from these stations is submitted to CPCB, New Delhi, through the Environmental Data Bank (EDB) system, ensuring timely reporting for national policy and pollution control efforts

Through the GEMS project, GPCB continues to provide essential data to guide water quality management and policy formulation at both state and national levels. The bifurcation of surface and groundwater monitoring ensures comprehensive surveillance of aquatic ecosystems and drinking water sources, reinforcing Gujarat's commitment to environmental protection.

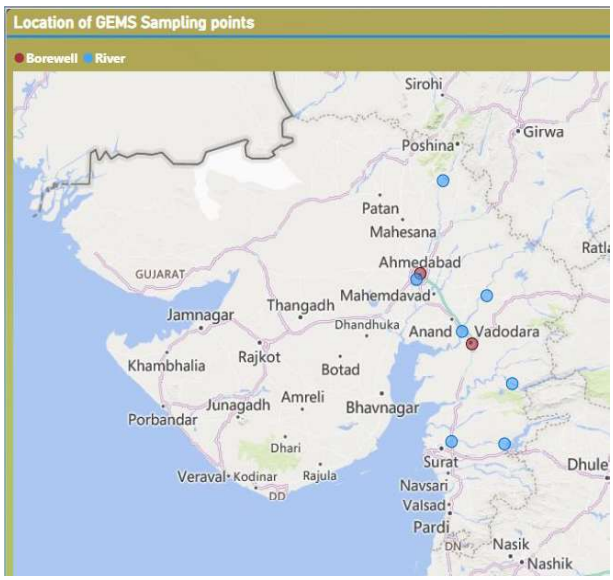


CHAPTER : VII

Environmental Quality Monitoring Programmes

7.2.2 Monitoring of Indian National Aquatic Resources System (MINARS) Project

GPCB in collaboration with CPCB, continues its comprehensive water quality monitoring under the Monitoring of Indian National Aquatic Resources System (MINARS) project. This long-term initiative covers surface water (River, Lake, Dam, Reservoirs, Canal etc.), groundwater (Bore well, Hand pump etc.) and even creeks across the state to assess and protect Gujarat's vital aquatic resources.

Under the MINARS project, GPCB has established an extensive water quality monitoring network covering various surface and groundwater sources. This comprehensive approach enables timely identification of pollution hotspots and supports data-driven interventions for water quality restoration and environmental management. GPCB remains committed to strengthening monitoring and improving water quality across Gujarat. Location wise annual average results of water monitoring carried out under the MINARS project of year 2024-25 is given in **Annexure – 20**.

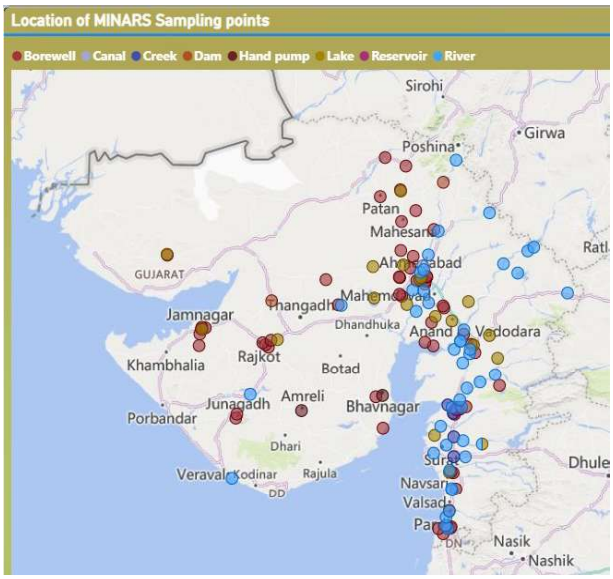

Overview of Water Quality Monitoring under MINARS


Type	Water Body Type	No. of Stations	Key Locations / Water bodies
Surface water	Rivers	44	Narmada, Sabarmati, Mahi, Tapi, Khari, Vishwamitri, Damanganga, Anas, Amaravati, Panam, Meshwo, Bhadar, Shedhi, Mindhola, Kim, Bhogavo, Dhadar, Ambika, Purna, Kaveri, Kolak, Par etc.
	Lakes/ Ponds	17	Kankaria, Chandola, Malav, Munsar, Ranmal, Hamirsar, Bindu sarovar, Ajwa, Sursagar, Gomti etc.
	Dams/ Reservoirs	3	Dharoi, Machhu-II, Reservoir of GIDC Ankleshwar
	Creeks	5	Amlakahdi, Vandkhadi, Masmakhadi, Baleshwar khadi etc.
	Canals	2	Tapi Canal, Narmada Canal
	Ramsar sites	2	Nalsarovar, Thol
Ground water	Borewells	57	GIDC and Urban/ Industrial clusters across Gujarat
	Hand Pumps	2	Hand pump of Bhavnagar, Amreli

7.2.3 Water quality under the Annual Status Project

GPCB undertakes annual statewide water quality assessments under the Annual Status Water Monitoring Project. This initiative covers surface water (rivers, lakes, reservoirs, creeks), groundwater (borewells, tubewells, open wells), and selected urban water bodies to evaluate ecological health and public safety.

Location wise annual average results of water monitoring carried out under the Annual status project for the year 2024-25 is given in **Annexure – 21.**

The Annual Water Quality Monitoring Project 2024–25 presents a comprehensive picture of aquatic ecosystem health in Gujarat. GPCB will continue to enhance surveillance and data transparency to support better pollution control strategies, ecosystem restoration, and public health protection.

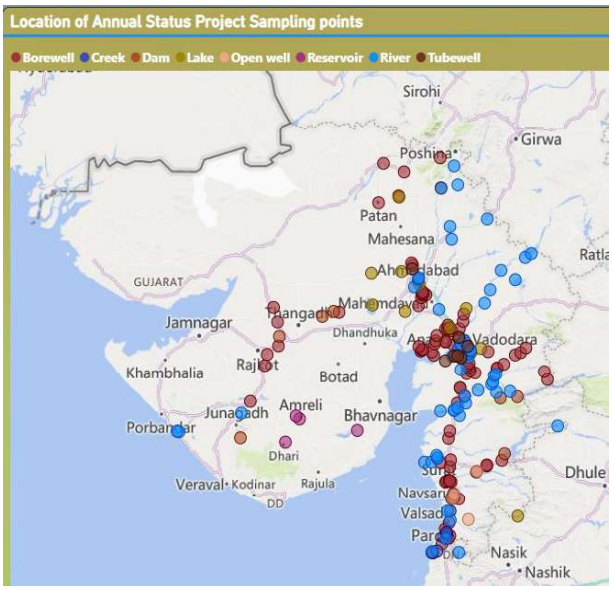

Overview of Water Quality Monitoring under Annual status project

Type	Water Body Type	No. of Stations	Key Locations / Water bodies
Surface water	Rivers	52	Narmada, Sabarmati, Mahi, Tapi, Khari, Vishwamitri, Damanganga, Anas, Amaravati, Panam, Meshwo, Bhadar, Shedhi, Dhadar, Par, Harnav, Karjan, Mini, Orsang, Uben, etc.
	Lakes/ Ponds	10	Kankaria, Sursagar, Bindu Sarovar, Malav, Shri Sayaji Sarovar, Moonsar, Gomti, etc.
	Dams/ Reservoirs	13	Sardar Sarovar Dam, Ukai Dam, Dharoi Dam, Machhu – I Dam, Karjan Dam, Anandpar Dam, Dholidhaja Dam, Nayka Dam, Reservoir at Khodiyar Dam, Reservoir at Shetrunjay Dam etc.
	Creeks	6	Bill Khadi, Kalakada Khadi, Kolai Khadi, Darotha Khadi, Tokar Khadi etc.
	Ramsar sites	2	Nalsarovar, Thol
Ground water	Groundwater	116	Borewells, Tubewells, open wells across Gujarat

CHAPTER : VII

Environmental Quality Monitoring Programmes

7.2.4 Water quality of Well water in Gujarat

GPCB conducts monitoring of well water quality across the state to assess its suitability for drinking and domestic use. Under this initiative, water samples are collected from a wide range of sources including borewells, tubewells, and open wells located in villages, towns, industrial zones, and rural habitations. Location wise annual average results of water monitoring carried out under the Well water monitoring for the year 2024-25 is given in **Annexure – 22.**




Overview of Well Water Quality Monitoring

Type	Water Body Type	No. of Stations	Key Locations
Ground water	Borewells	97	Urban & Rural Area across Gujarat
	Open Wells	6	Predominantly in Saurashtra, South Gujarat
	Tubewells	1	Panchmahal district

7.2.5 Environment Monitoring in Major Cities of Gujarat

GPCB conducts regular water quality monitoring across major cities of the state to assess the status of urban groundwater, surface water, and open wells. This initiative supports sustainable urban planning, public health safety, and pollution mitigation efforts. Location wise annual average results of water monitoring carried out for the Major cities of Gujarat for the year 2024-25 is given in **Annexure – 23.**

GPCB continues to strengthen its water monitoring network and urges local bodies and industries to adopt preventive measures, especially in high-risk zones.

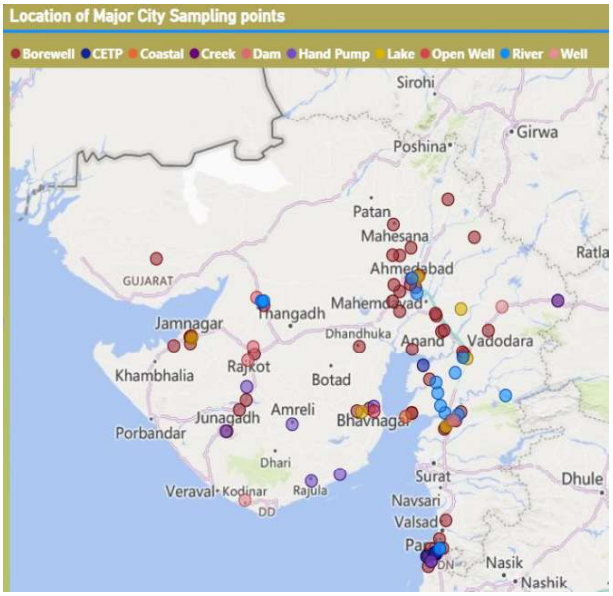

Overview of Water Quality Monitoring of Major cities

Type	Water Body Type	No. of Stations	Key Locations / Water bodies
Surface water	River	15	Sabarmati, Khari, Vishwamitri, Kaveri, Bhukhi, Dhadhar, Kalindri, Kolak, Damanganga etc.
	Lakes/ Ponds	6	Gomti talav, Lakhota talav, Ramsagar, etc.
	Dams	3	Aji-II Dam, Machchu-III Dam, Nyari-I Dam etc.
	Creek	1	Tokarkhadi
Ground water	Borewells and open wells	59	18+ districts i.e. Ahmedabad, Vadodara, Surat, Rajkot, etc.
	Hand Pumps	8	Amreli, Dahod, Junagadh, Gondal, Bhavnagar


CHAPTER : VII

Environmental Quality Monitoring Programmes

7.2.6 Bio monitoring of water bodies

To assess the ecological health of Gujarat's water bodies, GPCB undertakes biological monitoring. This program complements chemical assessments by focusing on aquatic life, particularly benthic macroinvertebrates, as indicators of water quality over time. Biological monitoring offers a long-term, cost-effective, and integrated view of water quality. Aquatic organisms reflect the cumulative impact of pollutants, making them ideal for tracking ecosystem health and supporting restoration planning. Location wise results of water monitoring carried out under the Bio monitoring project of year 2024-25 is given in

Annexure – 24.

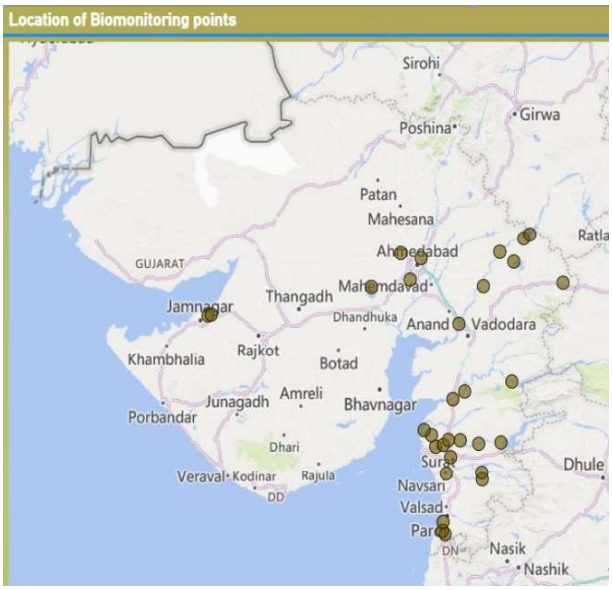

Biological Water Quality Criteria (BWQC)

Saprobic Score	Biological Water Quality Class	Expected level of Biodegradable Organic Matter (BOM) & DO
7 or more	Very Good	Very low BOM/High DO
5.0 to 6.9	Good	Low BOM/High DO
3.0 to 4.9	Moderate	Moderate BOM/DO
1.1 to 2.9	Poor	High BOM/Low DO
Less than 1	Severe	Very high BOM/Very Low or No DO

Overview of Water Quality Monitoring under Bio-monitoring

Water Body Type	No. of Monitoring Locations	Key Rivers / Lakes / Sites
Rivers	23	Narmada, Sabarmati, Mahi, Tapi, Anas, Panam, Damanganga, Kolak, Purna, Ambika, etc.
Lakes/ Ponds	2	Dudhiya Talav, Lalva Talav
Creeks	2	Masma Khadi, Baleshwar Khadi
Ramsar sites	4	Nalsarovar, Thol, Khijadiya

7.2.7 Coastal Monitoring

Gujarat, with India's longest coastline of 2,340.62 km, borders the Arabian Sea and hosts major ports such as Kandla, Mundra, Pipavav, Dahej and Hazira. This coastal region supports extensive industrial, urban, and port-based activities, which contribute to pollution through direct discharge or via rivers draining into the sea.

To assess the environmental impact and identify pollution hotspots, GPCB conducts coastal and estuarine water quality monitoring at strategically selected stations. This program is aligned with GPCB's commitment to sustainable coastal development and marine ecosystem protection. Details of the coastal water quality monitoring stations, along with the annual average values of major environmental parameters, are provided in the

Annexure – 25.

Continued surveillance, along with effective industrial effluent management and municipal sewage treatment, is vital to preserving Gujarat's coastal ecosystem.



Overview of Water Quality Monitoring under Coastal monitoring

Water Body Type	No. of Monitoring Stations	Key Locations
Coastal Waters	28	Dhuvaran, Veraval, Mundra, Sikka, Porbandar, etc.
Estuarine Waters	11	Narmada, Tapi, Damanganga, Kolak, Par
Industrial & Domestic Outfalls	17	Bhavnagar, Jamnagar, Porbandar, Kandla, Sarigam

ANNEXURE - 19

Results of water monitoring carried out under the GEMS project
(annual average of the year 2024-25)

Sr. No.	Water Body	Location	Parameters *			
			pH	DO	BOD	COD
River						
1.	River	River Narmada, Garudeshwar, Narmada	8.25	7.69	0.74	5.00
2.	River	River Tapi at Sherulla Bridge no. 46, Navsari	8.09	7.37	0.71	5.42
3.	River	River Tapi at Kathor N.H.48, Surat	7.93	7.10	1.10	7.00
4.	River	River Mahi at Sevaliya, Kheda	8.21	7.75	0.66	8.00
5.	River	River Mahi, Vasad, Anand	8.17	7.64	0.65	8.00
6.	River	River Sabarmati at Dharoi Dam, Mehsana	7.21	7.12	0.88	9.00
7.	River	River Sabarmati, Vasna - Narol Bridge, Ahmedabad	7.20	1.89	43.49	205.42
Borewell						
8.	Borewell	Borewell of Jain Temple, Govt. Guest House, Shahibaug, Ahmedabad	7.70	7.30	0.78	8.50
9.	Borewell	Borewell at Kamatibaug, Vadod ara	7.80	3.90	1.10	8.00

*Note: Except pH, all the parameters are expressed as mg/L.

ANNEXURE - 20

Results of water monitoring carried out under the MINARS project (annual average of the year 2024-25)

Sr. No.	Water Body	Location	Parameters *			
			pH	DO	BOD	COD
1.	Borewell	Borewell of Pirana Pumping Station	7.30	6.43	0.87	10.50
2.	Borewell	Borewell of VIA hall, GIDC Vatva	7.40	-	0.99	10.00
3.	Borewell	Borewell of GIDC Odhav	7.80	-	0.93	10.00
4.	Borewell	Borewell of TSDF, GESCL, Vatva	7.70	-	0.93	11.50
5.	Borewell	Borewell of TSDF, Naroda Enviro Project Ltd, Odhav	7.70	-	0.91	10.00
6.	Borewell	Borewell of Vinayak Jal Suddhikaran Sahakari Mandali Ltd., Bavla	7.41	3.05	0.99	8.50
7.	Borewell	Borewell of Shri Someshwar Rice Mill, Dhedhal, Bavla	7.18	5.21	1.22	9.00
8.	Borewell	Borewell of Alfa Ica P. Ltd. (Unit -II), Sanand	7.48	6.10	0.93	9.30
9.	Borewell	Borewell of L&T Ltd, Chacharavadi, Sanand	7.42	5.46	0.77	10.00
10.	Borewell	Borewell of GIDC Kansari, Khambhat	7.97	4.29	1.20	7.00
11.	Borewell	Borewell of GIDC Sojita	8.02	4.62	1.07	7.00
12.	Borewell	Borewell of Shri Jashwantbhai Parmar, Kalamsar, Khambhat	8.28	5.00	1.15	7.00
13.	Borewell	Borewell of Ankleshwar Industrial area (Ind. Carbon), Ankleshwar- Rajpipla road	7.47	-	0.65	5.00
14.	Borewell	Borewell of GIDC Jhagadia	7.34	-	0.54	5.00
15.	Borewell	Borewell of Rajpipla	7.39	6.35	0.83	5.00
16.	Borewell	Borewell of GIDC Panoli	8.37	7.23	0.80	5.00
17.	Borewell	Borewell of TSDF site, GIDC Ankleshwar	7.11	-	0.72	5.00
18.	Borewell	Borewell of GMB TSDF, Alang	7.64	4.30	1.20	4.00
19.	Borewell	Borewell of GIDC Vartej, Bhavnagar	7.64	4.20	1.35	6.00
20.	Borewell	Borewell of Santej	7.16	6.50	0.81	8.00
21.	Borewell	Borewell of GIDC Kalol	7.38	6.41	0.82	8.16
22.	Borewell	Borewell of Rameshwar Temple, Nr. Rameshwar Nagar	7.40	4.10	0.80	6.00
23.	Borewell	Borewell of GIDC Office, Shanker Tekri	7.30	3.40	1.30	7.00
24.	Borewell	Borewell of Mahavir Metallurgical, Dared GIDC, Phase III	7.05	4.10	1.40	6.00
25.	Borewell	Borewell of Shri Hitendrabhai Ker, Shivshakti park, New Samshan road, Jamnagar	7.96	4.00	0.80	7.00
26.	Borewell	Borewell of Kankeshwar Mahadev Temple, Vibhapar, Jamnagar	7.24	4.00	1.30	12.00

ANNEXURE - 20

Sr. No.	Water Body	Location	Parameters *			
			pH	DO	BOD	COD
27.	Borewell	Borewell of Varun Water Works, Talav Darvaja, Junagadh	7.46	-	1.10	9.59
28.	Borewell	Borewell of GIDC- II, Patel Remedies, Plot No. 317, Dolatpara, Junagadh	7.35	-	0.95	9.18
29.	Borewell	Borewell of Odhavpark society, Nr. Pramukh Swaminagar, Bhuj	7.80	3.10	1.80	9.50
30.	Borewell	Borewell of GIDC Mehsana	7.97	5.80	0.74	7.50
31.	Borewell	Borewell of Kadi Ind. Area	7.72	6.32	0.84	8.00
32.	Borewell	Borewell of Ranasan Ind. Area, Vijapur	7.26	6.79	0.80	8.50
33.	Borewell	Borewell of Visnagar Ind. Area	8.00	5.32	0.76	8.00
34.	Borewell	Borewell at Nadiad GIDC water works	7.96	4.69	-	7.50
35.	Borewell	Borewell of Santram mandir, Nadiad	7.73	6.66	-	7.50
36.	Borewell	Borewell of Navsari GIDC Industries Association office	7.43	-	2.35	11.50
37.	Borewell	Borewell of Kaliya wadi, Grid Road, Navsari	7.80	-	2.55	13.50
38.	Borewell	Borewell of Palanpur Nagarpalika	7.25	7.21	0.79	7.60
39.	Borewell	Borewell of Patan Nagarpalika	7.49	6.68	0.83	7.90
40.	Borewell	Borewell of Siddhpur Nagarpalika	7.56	7.01	0.77	8.00
41.	Borewell	Borewell of Deesa Nagarpalika	7.50	6.92	0.81	7.00
42.	Borewell	Borewell near STP Madhapar, Rajkot	7.56	3.75	1.00	7.78
43.	Borewell	Borewell of Raiya Circle, Rajkot	7.44	5.10	1.50	7.98
44.	Borewell	Borewell of Austin Engg., Aji GIDC, Rajkot	7.49	3.90	1.00	7.78
45.	Borewell	Borewell of RMC Solid Waste Site, Nakarawadi, Rajkot	7.54	3.80	1.05	11.99
46.	Borewell	Borewell of Coastal highway, Fansa char rasta	7.96	5.45	0.50	9.50
47.	Borewell	Borewell of Gayatri Pragna School	7.92	5.65	0.40	9.00
48.	Borewell	Borewell of Vinay Balmandir	7.44	-	0.95	9.76
49.	Borewell	Borewell near DCW Dhrangadhra	7.42	-	1.00	9.17
50.	Borewell	Borewell at Vadodara (Industrial- Nandesari)	7.44	4.43	2.18	78.00
51.	Borewell	Borewell near TSDF-NECL of Nandesari	7.27	3.34	2.35	85.00
52.	Borewell	Borewell of Vohragamdi	8.13	3.96	1.29	7.00
53.	Borewell	Borewell of Rajasthan Bhavan, Vapi	7.99	5.75	0.75	8.50
54.	Borewell	Borewell of Vapi Ind. Area (TSDF Site)	7.74	5.55	0.85	10.50

Sr. No.	Water Body	Location	Parameters *			
			pH	DO	BOD	COD
55.	Borewell	Borewell of Atul, Pardi	7.75	5.05	0.85	9.50
56.	Borewell	Borewell of Jilla Panchayat School, Kanta Faliya, Namdha	7.65	5.60	0.65	9.00
57.	Borewell	Borewell of GIDC, Antaliya water supply, Billimora, Gandevi, Navsari	7.74	-	2.45	9.50
58.	Canal	Tapi Canal at Umervada	8.31	7.69	0.82	5.10
59.	Canal	Narmada canal at Limbadia bridge	7.66	6.90	0.79	9.58
60.	Creek	Amlakahdi (Creek) at Pungam	7.50	3.44	10.40	37.83
61.	Creek	VandKhadi at Umervada	7.43	2.63	29.77	93.75
62.	Creek	Amlakahdi at low level bridge, Ankleshwar	7.42	3.26	5.81	33.00
63.	Creek	Baleshwar Khadi on N.H.No.8	7.87	6.00	1.90	10.00
64.	Creek	Masmakhadi, Olpad-Saras Road	7.90	6.20	2.20	15.00
65.	Dam	Dharoi Dam, Kheralu, Mehsana	7.74	6.91	0.73	8.58
66.	Dam	Machhu-II Dam, Morbi	7.50	6.64	1.96	9.51
67.	Hand pump	Hand pump at Rupani Circle, Bhavnagar	7.55	4.20	1.00	4.00
68.	Hand pump	Hand pump at Pitanpara, Amreli	7.55	4.30	1.50	6.00
69.	Lake	Kankaria Lake, Balvatika	8.70	5.86	12.34	73.42
70.	Lake	Chandola Lake	7.50	6.58	1.48	15.50
71.	Lake	Malav Talav, Dholka	8.57	5.95	6.01	62.50
72.	Lake	Munsar Lake, Viramgam	8.43	4.51	10.70	62.50
73.	Lake	Nalsarovar Lake, Sanand	7.96	6.11	5.13	42.00
74.	Lake	Verai Mata Talav, Aanad	8.31	6.86	1.09	20.00
75.	Lake	Ranmal Talav	7.53	4.80	1.40	12.00
76.	Lake	Hamirsar Talav, Bhuj	7.40	6.00	2.60	10.00
77.	Lake	Thol Tank at Kadi, Mehsana	7.70	4.63	7.27	39.80
78.	Lake	Kheta Talav, Nadiad	8.31	6.02	2.02	18.00
79.	Lake	Dhudhiya Talav, Navsari	8.01	7.40	0.92	7.75
80.	Lake	Bindu Sarovar, Siddhpur	7.46	6.52	0.95	15.60
81.	Lake	Moticher Lake Nr. Kapp Bridge	8.05	7.30	0.80	6.00
82.	Lake	Olpad village Pond at Olpad (Lalva Talav)	7.95	7.40	1.40	8.00

ANNEXURE - 20

Sr. No.	Water Body	Location	Parameters *			
			pH	DO	BOD	COD
83.	Lake	Ajwa Lake at Shri Sayaji Sarovar, Vadodara	8.23	7.57	1.00	9.00
84.	Lake	Sursagar Lake at Vadodara	8.14	6.75	1.44	21.00
85.	Lake	Wadhwana Wetland, Dabhoi	8.05	7.63	1.00	8.00
86.	Lake	Gomti Lake, Dakor	7.57	5.43	1.73	15.00
87.	Lake	Lake at Kuvadava	8.07	6.79	1.71	8.64
88.	Reservoir	Reservoir at GIDC Ankleshwar	8.24	7.56	0.80	5.16
89.	River	River Sabarmati at Railway Bridge	7.80	5.90	0.90	15.60
90.	River	River Sabarmati at Hansol Bridge	7.80	6.78	0.80	14.30
91.	River	River Khari at Village Lali	7.20	0.88	32.90	117.00
92.	River	River Sabaramati at Village Miroli	7.30	2.30	21.64	78.80
93.	River	River Sabarmati a/c river Vatrak at Vautha, Ta. Dholka	7.54	1.79	14.03	58.70
94.	River	River Mahi, Umeta	8.25	7.67	0.70	8.00
95.	River	River Narmada, Panetha	8.26	7.82	0.78	5.00
96.	River	River Amaravati before confluence near Dadhal	8.06	7.53	0.95	6.10
97.	River	River Amlakahdi at Pungam	7.57	5.00	11.20	45.91
98.	River	River Narmada at Nilkantheshwar Mahadev Temple, Zadeshwar, Bharuch	8.16	7.45	0.95	6.00
99.	River	River Narmada at Zanor (NTPC)	8.08	7.51	0.84	5.50
100.	River	River Sabarmati at Mahudi	7.52	6.54	0.75	8.25
101.	River	River Sabarmati at Chiloda bridge	7.60	6.30	0.87	9.70
102.	River	River Mahi at Ananadpuri	7.95	7.25	0.68	7.58
103.	River	River Mahi at Kadana (D/S)	7.92	7.22	0.64	7.58
104.	River	River Mahi at Virpur	8.07	7.31	0.66	7.58
105.	River	River Panam at Lunawada	8.12	7.07	0.73	7.67
106.	River	River Anas at Kushalgadh	8.32	7.19	0.78	7.92
107.	River	River Sabarmati at Kheroj Bridge	7.40	7.07	0.75	9.00
108.	River	River Meshwo at Shamlaji	7.54	6.71	0.73	8.83
109.	River	River Bhadar at Dublipat	7.78	5.69	8.11	36.03
110.	River	Triveni Sangam at Somnath, Nr. Triveni Sangam Ghat, Gir Somnath	7.50	6.60	1.94	11.32

Sr. No.	Water Body	Location	Parameters *			
			pH	DO	BOD	COD
111.	River	River Shedhi at Kheda-Matar road	7.93	4.39	4.83	35.00
112.	River	River Tapi at Mandvi	8.02	7.10	1.00	6.00
113.	River	River Tapi at Varachha Bridge	7.94	7.10	1.40	8.00
114.	River	River Tapi at Nr. Kapp Bridge	8.03	7.30	0.80	5.00
115.	River	River Tapi at ONGC Bridge, Surat	7.80	6.60	1.80	19.00
116.	River	River Mindhola at S.H., Surat-Navsari Road, Sachin	7.91	5.70	2.50	20.00
117.	River	River Kim at Sahol Bridge	7.96	6.20	2.20	14.00
118.	River	River Bhogavo	7.47	6.16	2.46	15.96
119.	River	River Narmada at Chandod	8.06	7.77	1.00	8.00
120.	River	River Vishwamitri at Khalipur	7.77	2.34	5.87	36.00
121.	River	River Vishwamitri at Asod Bridge	8.08	7.02	1.00	11.00
122.	River	River Mahi at Mujpur	8.30	7.28	1.00	12.00
123.	River	River Mahi at Sherkhi, Nr. Sindhrot bridge	8.26	7.69	1.00	9.00
124.	River	River Mahi at Parthampura (Rania) Bridge, GSFC Water Works	8.28	7.97	1.00	8.00
125.	River	River Dhadhar at Kothwada	7.78	2.95	4.00	35.00
126.	River	River Ambika at Billimora- Amalsad Bridge	7.74	6.89	1.57	15.33
127.	River	River Purna at Navsari- Surat state highway bridge	7.92	7.05	1.25	10.58
128.	River	River Kaveri at Billimora- Valasd road bridge	8.11	6.88	1.46	13.17
129.	River	River Damanganga at Kachigam Bridge	7.78	6.13	1.24	24.17
130.	River	River Damanganga at GIDC Weir, Vapi	7.86	7.03	0.80	9.33
131.	River	River Kolak at Pataliya Bridge	7.84	6.83	1.07	13.83
132.	River	River Par at Rly. Bridge, Atul	7.73	6.65	1.33	23.92

*Note: Except pH, all the parameters are expressed as mg/L.

ANNEXURE - 21

Results of water monitoring carried out under the Annual Status project (annual average of the year 2024-25)

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2- N	NO_3-N	TC	FC	F
1.	Borewell of Jain Temple, Govt. Guest House, Shahibaug, Ahmedabad	7.70	7.30	0.78	8.50	585	0.42	0.76	0.070	0.62	<2	<2	0.60
2.	Borewell of Chosar Gram Panchayat	7.40	-	0.89	9.75	1,808	-	-	0.070	0.56	-	-	0.91
3.	Borewell of Devdi Gram Panchayat	7.60	-	1.07	9.75	1,242	0.64	-	0.100	0.79	-	-	1.02
4.	Borewell of Gamdi Gram Panchayat	7.50	-	0.79	10.80	1,837	-	-	0.070	0.63	-	-	1.07
5.	Borewell of Istolabad Gram Panchayat	7.30	-	0.90	9.75	2,451	0.49	-	0.050	0.46	-	-	0.95
6.	Borewell of Lali Gram Panchayat	7.70	-	0.83	9.75	1,964	1.48	-	0.120	0.66	-	-	1.21
7.	Borewell of Navagam Gram Panchayat	7.40	-	0.87	10.00	2,206	0.49	-	0.070	0.64	-	-	0.75
8.	Borewell of Ropada Gram Panchayat	7.50	-	0.99	10.30	1,736	-	-	0.070	0.63	-	-	0.68
9.	Borewell of Anand Nagarpalika, Near Thakkar wadi, Anand	7.70	4.18	-	7.00	690	BDL	-	0.010	0.86	<2	<2	0.36
10.	Borewell of Anand Nagarpalika, Anand-Sojitra Road, Anand	7.35	4.91	-	8.00	864	0.31	-	0.010	0.34	<2	<2	0.59
11.	Borewell of Ankalv Nagarpalika Water Works, Anklav, Anand	7.62	6.56	-	8.00	668	0.28	-	0.020	0.18	<2	<2	0.63
12.	Borewell of Borsad Nagarpalika, Borsad, Anand	7.84	5.88	-	8.00	828	0.48	-	0.010	0.74	<2	<2	0.80
13.	Borewell of Dharmaj village, Nr. Jalaram Temple, Anand	7.85	5.01	-	8.00	1,166	0.42	-	0.020	2.82	<2	<2	1.04
14.	Borewell of GIDC Kansari, Anand	8.00	4.70	-	7.54	2,760	0.52	-	0.020	0.52	<2	<2	0.66
15.	Borewell of GWSSB at Dhuvaran, Anand	8.25	4.04	-	8.00	892	BDL	-	0.010	0.96	<2	<2	0.35
16.	Borewell of Hadgud village	7.83	3.30	-	7.00	780	BDL	-	0.008	4.65	<2	<2	0.40
17.	Borewell of Kalamsar village, Khambhat, Anand	8.33	4.00	-	8.00	1,298	BDL	-	0.010	0.84	<2	<2	1.01
18.	Borewell of Karamsad Sardar Nagar Co.Op. Hou. Society Ltd., Karmsad, Anand	7.39	3.42	-	7.00	1,042	BDL	-	0.001	1.63	<2	<2	0.39

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
19.	Borewell of Khambhat Nagarpalika, Khambhat, Anand	7.78	7.80	-	8.00	2,038	0.48	-	0.010	1.24	<2	<2	7.78
20.	Borewell of Lambhvel village, Anand	7.91	4.09	-	6.00	514	BDL	-	0.001	14.02	<2	<2	0.42
21.	Borewell of Ode Nagarpalika, Anand	7.91	4.81	-	6.00	662	BDL	-	0.001	4.73	<2	<2	0.44
22.	Borewell of ONGC Colony, Khambhat, Anand	7.92	5.97	-	7.00	2,382	0.62	-	0.020	0.18	<2	<2	1.08
23.	Borewell of Petlad Town, Opp. Ranchodraiji Mandir, Anand	7.90	6.23	-	8.00	850	0.50	-	0.010	0.10	<2	<2	0.50
24.	Borewell of Raymon Patel Gelatine, at Vasad, Anand	7.07	4.43	-	7.00	6,258	BDL	-	0.360	0.01	<2	<2	0.86
25.	Borewell of Sarsa Gram panchayat, Anand	7.38	3.62	-	12.00	570	BDL	-	0.001	4.91	<2	<2	0.47
26.	Borewell of Shahid Baug, Khambhat, Anand	7.50	7.31	-	7.00	2,922	0.44	-	0.020	1.84	<2	<2	0.70
27.	Borewell of Sokhada, Anand	8.04	6.40	-	8.00	1,536	0.32	-	0.020	0.50	<2	<2	0.69
28.	Borewell of Surya Mandir, Borsad, Anand	7.80	5.43	-	7.00	970	0.44	-	0.020	1.68	<2	<2	1.45
29.	Borewell of Umeta Gram panchayat office, Umeta, Anklav, Anand	8.09	4.34	-	8.00	788	BDL	-	0.010	0.90	<2	<2	0.40
30.	Borewell of Umreth water works, Anand	7.26	4.28	-	6.00	1,576	BDL	-	0.015	4.21	<2	<2	0.38
31.	Borewell of V.V.Nagar vtc swimming pool, Mota bazaar	7.58	3.62	-	6.00	870	BDL	-	0.004	1.83	<2	<2	0.32
32.	Borewell of Virsad village, Anand	8.02	5.01	1.00	7.00	732	BDL	0.84	0.010	0.29	<2	<2	0.34
33.	Borewell of Gram Panchayat near Motivasat, Palej, Bharuch	8.44	6.90	-	5.00	1,906	-	-	0.030	1.07	<2	<2	0.99
34.	Borewell of Gram Panchayat near Nirala park, Palej, Bharuch	8.49	6.80	-	5.00	1,386	-	-	0.080	1.25	<2	<2	BDL
35.	Borewell of Haldarva water works, Haldarva, Bharuch	8.35	6.70	-	5.00	2,688	-	-	0.380	2.19	<2	<2	1.95
36.	Borewell of Zanor water works, Zanor, Bharuch	8.46	7.90	-	5.00	1,350	-	-	0.050	2.04	<2	<2	0.06
37.	Borewell of Dhanot, Gandhinagar	7.45	6.35	0.84	8.00	1,503	0.35	0.44	-	0.62	<2	<2	0.97
38.	Borewell of Kalol Nagarpalika, Gandhinagar	7.55	6.50	0.89	7.50	958	0.42	0.58	0.060	0.55	<2	<2	0.54
39.	Borewell of Radheshyam Textile, Dhareshwar GIDC, Jetpur	7.20	3.30	1.20	7.97	948	0.28	1.68	0.017	1.40	<1.8	<1.8	0.47
40.	Borewell of Atul Pharmaceutical, Wankaner, Morbi	7.26	3.70	1.00	9.18	1,924	1.12	1.88	0.020	1.40	-	-	0.36

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
41.	Borewell of GIDC Halwad (Sursagar dairy), Morbi	7.28	3.70	1.00	9.58	3,092	0.56	-	0.017	0.22	-	-	1.26
42.	Borewell of Matrix Cera Anemal Company, Rafaleshwar GIDC, Morbi	7.67	3.80	1.10	9.98	1,192	0.56	0.84	0.020	1.34	-	-	0.09
43.	Borewell of Desai Talav, Ghelkhadi Water Works	8.02	-	2.60	14.00	852	0.28	0.56	0.045	0.05	<2	<2	0.12
44.	Borewell of Chikhali Water Works	8.20	-	2.40	9.00	692	0.28	0.56	0.043	0.07	<2	<2	0.36
45.	Borewell of Chovishi Gram Panchayat	8.37	-	2.30	12.00	1,024	0.28	0.56	0.021	0.04	<2	<2	0.10
46.	Borewell of Gandevi Tel. Exchange	8.12	-	2.40	11.00	834	0.28	0.56	0.045	0.06	<2	<2	0.13
47.	Borewell of GIDC Antalia, Navsari	8.16	-	2.50	15.00	1,400	0.28	0.56	0.075	0.08	<2	<2	0.21
48.	Borewell of GIDC Kabilpore	8.24	-	2.80	14.00	1,196	0.28	0.56	0.056	0.07	<2	<2	0.25
49.	Borewell of Kaliyawadi, Navsari	8.37	-	2.40	12.00	1,318	0.28	0.56	0.035	0.05	<2	<2	0.25
50.	Borewell of Main Tel. Exchange, Billimora	8.20	-	2.70	10.00	534	0.28	0.56	0.028	0.04	<2	<2	0.28
51.	Borewell of Railway station, Vyara, Tapi	8.00	-	2.20	12.00	426	0.28	0.56	0.056	0.08	<2	<2	0.30
52.	Borewell of Sandhkuva Tel. Exchange	8.06	-	2.50	14.00	1,696	0.28	0.56	0.014	0.15	<2	<2	0.26
53.	Borewell of Taluka Panchayat Songadh	8.04	-	2.30	10.00	428	0.28	0.56	0.051	0.07	<2	<2	0.30
54.	Borewell of Valod Taluka Panchayat	8.11	-	2.70	12.00	560	0.28	0.56	0.045	0.06	<2	<2	0.15
55.	Borewell of Vyara Circuit House, Tapi	8.08	-	2.10	9.00	396	0.28	0.56	0.085	0.10	<2	<2	0.26
56.	Borewell of Ambaji Nagarpalika	7.49	7.90	-	8.00	442	-	-	0.050	0.55	<2	<2	0.13
57.	Borewell of Deesa Nagarpalika	7.75	7.85	-	8.00	586	-	-	0.050	0.37	<2	<2	0.43
58.	Borewell of Palanpur Nagarpalika	7.62	8.06	-	7.00	954	-	-	0.090	0.68	<2	<2	0.58
59.	Borewell of Patan Nagarpalika	7.79	7.92	-	8.00	1,178	-	-	0.120	0.91	<2	<2	0.50
60.	Borewell of Siddhpur Nagarpalika	7.60	8.00	-	9.00	774	-	-	0.130	1.02	<2	<2	0.34
61.	Borewell of Milan Ind. GIDC, Kuvadawa, Rajkot	7.38	3.50	1.00	8.36	910	0.28	1.68	0.021	0.03	<1.8	<1.8	0.44
62.	Borewell of Veraval (Shapar), Gram Panchayat, Rajkot	7.12	3.70	1.00	9.16	1,484	0.28	1.68	0.012	1.40	<1.8	<1.8	1.67

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
63.	Water supply of Aji GIDC Industrial Association Water Supply Well No. 1 Aji GIDC, Rajkot	7.51	3.20	1.10	8.82	1,172	6.72	11.28	0.022	0.39	<1.8	<1.8	0.57
64.	Borewell of Sarigam Gram Panchayat at Sarigam	7.93	-	-	9.00	542	-	-	0.010	0.33	-	-	0.54
65.	Borewell of water works, at Umbergaon	8.45	-	-	9.00	244	-	-	0.010	0.34	-	-	0.26
66.	Borewell of Neelam Fiber, Kim Ind. Area	8.36	4.10	2.60	14.00	2,176	0.56	1.12	0.047	0.12	<2	<2	0.21
67.	Borewell of Pandesara Industrial area at SGTPA Hall, Pandesara, Surat	8.18	3.00	2.80	14.00	3,274	1.40	1.68	0.102	0.14	<2	<2	0.29
68.	Borewell of PHC Kadodara	8.47	4.20	2.30	10.00	1,006	0.28	0.56	0.076	0.12	<2	<2	0.19
69.	Borewell of Piramal Glass Tarsadi at Kosamba	7.99	4.20	2.70	12.00	2,092	0.28	0.56	0.016	0.05	<2	<2	0.28
70.	Borewell of SIEL GIDC Sachin	7.78	3.20	2.80	16.00	3,072	0.56	1.12	0.100	0.18	<2	<2	0.25
71.	Borewell of Amrapura Gra m panchayat, Vadodara	7.90	3.22	1.00	15.00	1,332	BDL	5.14	0.010	3.80	<2	<2	0.39
72.	Borewell of Angadh, Vadodara	8.24	4.01	1.00	8.00	772	BDL	5.12	BDL	4.20	<2	<2	0.48
73.	Borewell of Bamangam, Vadodara	7.41	4.02	1.00	8.00	1,360	BDL	4.30	BDL	4.00	<2	<2	0.46
74.	Borewell of Bhimpura Gram Panchayat, Ta. Padra, Vadodara	7.29	4.04	1.00	8.00	702	BDL	5.20	BDL	3.00	<2	<2	0.49
75.	Borewell of Bodeli Gram Panchayat, Chhotaudepur	7.69	-	1.00	7.00	334	BDL	5.14	BDL	4.10	<2	<2	0.53
76.	Borewell of Chhotaudepur, Nr. Referral Hospita l & CHC	7.85	-	1.00	8.00	304	BDL	1.80	BDL	1.10	<2	<2	0.78
77.	Borewell of Dashrath Gram panchayat, Vadodara	8.09	4.11	1.00	8.00	2,528	BDL	3.10	BDL	1.20	<2	<2	0.74
78.	Borewell of Dhanuka's Chali, Karachiya, Vadodara	8.38	4.22	1.00	8.00	1,172	BDL	6.20	BDL	4.80	<2	<2	0.82
79.	Borewell of Enviro Infra-Structure Co. Ltd, Umaraya, Ta. Padra, Vadodara	7.33	3.76	1.00	8.00	2,596	1.24	7.22	BDL	4.40	<2	<2	0.83
80.	Borewell of GIDC Por, Ramangamadi, Vadodara	8.50	3.38	1.00	8.00	1,102	BDL	4.48	0.020	3.10	<2	<2	0.86
81.	Borewell of Gram Panchayat Water Works, Bajwa, Vadodara	8.03	4.56	1.00	8.00	2,126	BDL	6.40	1.200	3.46	<2	<2	0.64
82.	Borewell of Grampanchayat Kandari, Vadodara	7.45	4.07	1.00	7.00	934	BDL	4.60	BDL	3.22	<2	<2	0.62
83.	Borewell of Itola Grampanchayat, Vadodara	7.58	3.66	1.00	8.00	1,128	BDL	5.18	BDL	4.60	<2	<2	0.92

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
84.	Borewell of Kadipani, Chhotaudepur	7.09	-	1.00	8.00	430	BDL	4.16	BDL	3.10	<2	<2	0.51
85.	Borewell of Karachiya Gram Panchayat Water Works, Vadodara	8.26	4.69	1.00	8.00	942	BDL	3.42	0.140	1.62	<2	<2	0.39
86.	Borewell of Kayavarohan, Ta. Karjan, Vadodara	7.40	4.16	1.00	8.00	830	BDL	5.40	BDL	4.18	<2	<2	0.81
87.	Borewell of Keshrisinh Padhiyar, Bhimpura, Vadodara	7.11	3.90	1.00	8.00	712	BDL	3.12	0.020	2.10	<2	<2	0.52
88.	Borewell of Koyali Gram panchayat Water Works, Vado dara	8.14	4.63	1.00	8.00	864	BDL	4.20	BDL	3.16	<2	<2	0.53
89.	Borewell of Kwant Gram Panchayat, Chhotaudaipur	7.45	-	1.00	7.00	1,218	BDL	1.70	BDL	0.84	<2	<2	0.94
90.	Borewell of Padmala Gram panchayat Waterworks, Vadodara	8.15	4.09	1.00	8.00	1,442	BDL	5.80	BDL	3.16	<2	<2	0.52
91.	Borewell of Padra Nagarpalika Water Works, Vadodara	7.17	4.25	1.00	8.00	1,992	BDL	5.10	BDL	3.16	<2	<2	0.86
92.	Borewell of Pavi-Jetpur, Chhotaudepur	7.73	-	1.00	7.00	436	BDL	2.00	0.010	1.43	<2	<2	0.77
93.	Borewell of Shri Punjabhai Patel Undera, Vadodara	8.04	4.52	1.00	8.00	1,228	BDL	6.14	BDL	3.20	<2	<2	0.39
94.	Borewell of Rampura Gram Panchayat	8.09	4.11	1.00	8.00	506	BDL	2.80	BDL	0.40	<2	<2	1.33
95.	Borewell of Sangma, Gam Panchayat, Ta. Padra, Vadodara	7.80	3.76	1.00	8.00	1,220	BDL	4.16	BDL	3.12	<2	<2	1.42
96.	Borewell of Sankheda Vari Gruh, Sankheda, Chhotaudaipur	7.57	-	1.00	7.00	776	BDL	5.84	BDL	5.10	<2	<2	0.88
97.	Borewell of Undera Gram Panchayat, Vadodara	8.20	4.47	1.00	8.00	814	BDL	6.40	BDL	3.60	<2	<2	0.29
98.	Borewell of Vakal Vidhyalay, Baj wa, Vadodara	8.34	4.42	1.00	8.00	1,462	BDL	5.40	BDL	3.10	<2	<2	0.53
99.	Borewell of Varnama, Vadodara	7.40	3.59	1.00	8.00	730	BDL	2.14	BDL	1.86	<2	<2	0.69
100.	Borewell of Waghodia, Vadodara	6.75	3.84	1.00	8.00	1,074	BDL	4.94	BDL	4.10	<2	<2	0.73
101.	Borewell of Shri Bhagubhai Patel at Kocharva	7.44	-	-	10.00	1,070	-	-	0.008	0.23	-	-	0.30
102.	Borewell of Govt. Borewell, Bhandariwad-Balitha	7.36	-	-	9.00	438	-	-	0.006	0.30	-	-	0.26
103.	Borewell of Kotashwar Mahadev Temple, Vattar	7.85	-	-	7.00	424	-	-	0.014	0.29	-	-	0.33
104.	Borewell of Rajasthan Bhavan, Chanod Area	7.93	-	-	8.00	482	-	-	0.022	0.31	-	-	0.25
105.	Water supply of Pardi Municipality	7.11	-	-	7.00	310	-	-	BDL	0.34	-	-	0.22

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
106.	Darotha Khadi at Eklara	8.16	7.10	0.90	10.00	510	1.12	2.24	0.010	0.34	280	23	-
107.	Tokar Khadi at Khatalwada	8.21	7.00	0.90	10.00	1,510	3.36	4.48	0.010	0.35	240	21	-
108.	Bill Khadi at Chharwada Bridge	7.17	5.50	5.00	81.00	1,512	10.64	11.76	0.014	0.15	170	43	0.32
109.	Bill Khadi at N.H.No. 8 at Morai	7.46	5.50	5.00	66.00	736	11.20	-	-	-	-	-	-
110.	Kalakada Khadi at Kachigam Bridge Vapi	7.35	6.30	2.40	80.00	690	17.36	19.04	0.009	0.30	140	34	0.36
111.	Kolai Khadi at N.H.No. 8 Bridge at Gundlav	7.89	5.60	2.70	38.00	884	1.96	-	-	-	-	-	-
112.	Karjan Dam, at Karjan, Narmada	8.32	7.52	1.00	5.00	222	BDL	-	0.038	0.96	13	2	0.23
113.	Sardar Sarovar Dam, Kevadia, Narmada	8.48	7.59	1.00	5.00	240	BDL	-	0.032	0.86	11	2	0.18
114.	Anandpar Dam, Junagadh	7.41	6.60	1.90	10.35	608	0.28	0.56	0.017	0.28	46	14	0.17
115.	Dharoi Dam, Mehsana	7.74	6.91	0.73	8.58	265	0.75	1.09	0.072	0.66	9	<1.8	0.44
116.	Machchu Dam – 1, Jalsika, Wankaner, Morbi	7.91	6.80	1.80	7.98	428	1.12	1.88	0.040	0.23	-	-	0.28
117.	Ukai Dam, Tapi	8.15	7.30	0.60	5.00	220	1.40	1.68	0.024	0.05	<1.8	10	0.19
118.	Dholidhaja Dam	7.41	6.70	1.80	7.58	176	0.28	0.56	0.050	0.23	94	22	0.08
119.	Nayka Dam	7.26	6.60	1.80	7.58	188	0.28	0.56	0.050	0.23	47	13	0.39
120.	Shree Sayaji Sarovar, Ajwa, Vadodara	8.03	7.68	1.00	8.00	196	0.56	1.72	0.010	0.42	13	2	BDL
121.	Auranga Weir, Abrama	8.25	-	-	8.00	242	-	-	BDL	0.24	-	-	0.20
122.	Kankaria Lake	8.70	5.86	12.34	73.42	1,653	1.31	1.80	0.060	0.56	>1600	>1600	0.77
123.	Malav Talav	9.01	7.14	1.63	22.00	1,860	0.74	1.12	0.030	0.38	340	120	1.12
124.	Moonsar Lake	8.51	7.32	1.06	25.00	1,920	0.56	0.78	0.060	0.44	230	70	1.02
125.	Nalsarovar Lake	8.04	7.35	1.58	32.00	1,866	0.90	1.12	0.050	0.55	350	110	1.89
126.	Veraimata Lake, Anand	8.29	7.70	1.00	28.00	832	BDL	0.58	0.010	0.34	>1600	>1600	BDL
127.	Thol Lake, Mehsana	7.70	4.63	7.27	39.80	643	2.00	3.24	0.077	0.61	308	92	0.58

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
128.	Lake Gomti Dakor	7.09	6.67	1.00	7.00	290	BDL	0.78	0.010	0.38	>1600	900	0.14
129.	Bindu Sarovar	7.83	7.58	-	13.00	1,142	-	-	0.060	0.55	170	21	0.48
130.	Padara lake, Padara, Vadodara	8.26	2.63	5.00	51.00	1,680	BDL	2.12	BDL	0.30	>1600	920	0.62
131.	Sursagar lake, Vadodara	8.14	6.75	1.45	20.00	398	BDL	2.48	0.160	1.76	500	56	0.33
132.	Lake of Saputara	8.07	7.00	0.60	10.00	140	0.84	1.40	BDL	0.30	27	6	-
133.	Open well of Antalia Water Works	8.18	-	2.30	8.00	888	0.28	0.56	0.045	0.06	<2	<2	0.30
134.	Open well of Gandevi water works	8.18	-	2.10	11.00	832	0.28	0.56	0.045	0.05	<2	<2	0.15
135.	Open well of Valod Ciruit House	8.18	-	2.50	11.00	536	0.28	0.56	0.045	0.05	<2	<2	0.27
136.	Open well of Dharampur water Works	8.15	-	-	8.00	996	-	-	BDL	0.33	-	-	0.24
137.	Reservoir at Kamnath Dam Amreli	7.58	4.10	2.30	8.00	292	1.68	2.24	-	0.69	<1.8	<1.8	0.42
138.	Reservoir at Khodiyar Dam, at Dhari, Amreli	7.62	4.20	1.80	8.00	280	1.68	2.24	-	0.71	<1.8	<1.8	0.34
139.	Reservoir at Shetrunjay Dam Palitana	7.43	4.80	1.20	8.00	346	1.68	2.80	-	0.78	-	-	0.38
140.	Reservoir at Vadi Dam Mangvapur, Amreli	7.46	4.30	2.10	8.00	202	1.12	2.24	-	0.68	<1.8	<1.8	0.34
141.	River Sabarmati at Rly. Bridge	7.80	5.90	0.90	15.60	227	1.10	1.60	0.100	0.70	185	41	0.50
142.	River Sabarmati at V.N.Bridge	7.20	1.89	43.49	205.42	733	11.01	17.60	0.100	0.60	>1600	>1600	0.61
143.	River Amravati at Dadhal village	8.06	7.53	0.95	6.10	555	BDL	1.23	0.120	1.16	140	47	0.41
144.	River Karjan (D/S), Rajpipla, Narmada	8.21	7.33	1.00	5.00	290	BDL	-	0.042	0.74	20	4	0.27
145.	River Narmada at Garudeshwar, Narmada	8.25	7.69	0.74	5.00	195	BDL	0.84	0.270	0.78	57	18	0.20
146.	River Narmada at Golden Bridge, Bharuch	8.48	7.11	1.00	5.00	252	BDL	-	0.460	1.20	79	13	0.33
147.	River Narmada at Panetha, Panetha, Narmada	8.26	7.82	0.78	5.00	198	BDL	0.98	0.280	0.71	48	16	0.25
148.	River Narmada at Poicha, Narmada	8.36	7.48	1.00	5.00	238	BDL	-	0.047	0.89	24	4	0.19
149.	River Narmada at Zanor, Bharuch	8.21	8.21	0.80	6.00	208	BDL	0.56	0.060	0.96	78	20	BDL

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
150.	River Narmada at Golden Bridge, Bharuch	8.25	7.50	1.20	7.00	208	BDL	1.12	0.090	1.78	270	110	1.96
151.	River Narmada at Kabirvad, Bharuch	8.48	8.00	0.90	6.00	268	BDL	0.56	0.090	0.70	120	68	BDL
152.	River Narmada at Nilkantheshwar Mahadev, Zadeshwar, Bharuch	8.48	8.50	1.00	6.00	236	BDL	1.12	0.070	0.81	140	45	BDL
153.	River Narmada at Village Bhadbhut, Bharuch	8.38	6.90	1.30	8.00	1,356	BDL	1.12	0.078	1.86	93	40	BDL
154.	River Anas at Khusalgadh	8.10	7.46	1.00	8.00	328	BDL	1.40	0.010	0.40	33	7	-
155.	River Mahi at Anandpuri	7.97	7.53	1.00	8.00	240	BDL	0.68	0.010	0.40	17	2	-
156.	River Mahi at Kadana Dam (D/S)	8.15	7.64	1.00	8.00	242	BDL	1.10	0.010	0.40	17	2	-
157.	River Mahi at Virpur	8.16	7.72	1.00	8.00	262	BDL	1.68	0.010	0.58	17	4	-
158.	River Panam at lunawada	8.23	7.54	1.00	5.00	294	BDL	0.48	0.010	0.20	21	4	-
159.	River Harnav at Khedbrahma, Sabarkantha	7.27	7.02	0.91	8.00	448	0.56	0.90	0.080	0.66	12	<1.8	0.56
160.	River Hathmati at Himmatnagar,Sabarkan tha	7.53	6.61	0.71	7.00	440	0.70	1.12	0.070	0.49	12	<1.8	0.62
161.	River Khari at Ghadi, Ta.Talod, Sabarkantha	7.56	6.73	0.82	22.00	1,038	2.44	4.28	0.070	2.10	21	<1.8	0.39
162.	River Meshwo (D/S) of Meshwo Dam, Shamlaji, Ta.Bhiloda, Arvalli	7.23	6.67	0.71	8.50	225	0.56	0.84	0.080	0.62	14	<1.8	0.45
163.	River Sabarmati at Kheroj Bridge, Ta.Khedbrahma, Sabarkantha	9.45	7.19	0.76	8.00	722	0.56	0.90	0.110	0.86	7	<1.8	1.03
164.	River Uben at Village Chowki	7.33	4.48	18.00	62.00	5,120	0.56	0.84	0.044	0.24	94	33	1.31
165.	River Sabarmati, at Dharoi Dam, Mehsana	7.21	7.12	0.88	9.00	252	BDL	BDL	0.050	0.31	6	<1.8	0.36
166.	River Mahi at Sevalia	8.04	9.26	1.00	8.00	294	BDL	1.08	0.010	0.28	70	8	0.33
167.	River Mahi at Wanakbori Dam	7.86	8.70	1.00	8.00	264	0.22	0.86	0.010	0.26	<2	<2	0.74
168.	River Shedhi at Mahemdabad- Nadiad road	7.59	4.22	4.08	81.00	494	1.24	2.98	0.010	0.60	>1600	>1600	0.77
169.	River Tapi, at Nizar, Taloda road Bridge, Nr. Village Hatoda	7.56	7.20	0.80	8.00	342	0.56	0.84	-	0.27	12	50	0.26
170.	River Bhadar at Garej village	7.86	5.54	1.90	15.60	4,768	0.60	-	0.009	0.28	6	2	-
171.	River Bhadar at Ratiya village (Esturine zone)	7.76	5.41	2.13	18.10	14,949	0.61	-	0.016	0.30	4	<1.8	-

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
172.	River Varoli at Sanjan	8.11	7.11	0.90	10.00	288	1.12	1.68	0.010	0.34	220	17	-
173.	River Tapi at L&T Jetty (E sturine zone)	7.11	6.00	2.60	22.00	33,812	0.56	1.12	0.042	0.07	32	10	0.34
174.	River Tapi at ONGC Bridge, Surat (Esturine zone)	7.80	6.60	2.10	20.00	34,142	0.56	1.12	0.102	0.14	31	12	0.35
175.	River Tapi at Sardar Bridge (Esturine zone)	8.02	6.50	1.80	14.00	12,226	0.67	1.42	0.110	0.21	113	27	0.29
176.	River Tapi at Swami Vivekanand Bridge (Esturine zone)	8.10	6.60	1.90	14.00	12,110	0.60	1.40	0.100	0.20	117	29	0.30
177.	River Tapi at Weir cum Causeway	8.15	6.50	2.00	11.00	512	0.56	1.12	0.058	0.11	39	12	0.19
178.	River Dhadhar at Kothwada, Ta. Padra, Vadodara	7.34	3.33	4.00	28.00	712	1.10	2.52	0.010	1.30	>1600	>1600	0.64
179.	River Mahi at Mujpur, Vadodara	8.08	7.24	1.00	9.00	412	BDL	2.30	0.010	1.35	240	22	0.24
180.	River Mini at Angadh, Vadodara	7.84	3.74	2.22	31.00	1,206	0.60	4.98	0.010	3.28	240	50	0.86
181.	River Mini at Sankarda, Vadodara	8.17	7.11	1.00	8.00	502	BDL	0.46	BDL	0.28	300	23	0.32
182.	River Mini at Sindhrot Bridge Vadodara	8.13	-	8.00	89.00	1,132	BDL	2.98	0.010	1.20	300	23	0.87
183.	River Narmada at Chanod, Ta. Dabhoi, Vado dara	8.06	7.77	1.00	8.00	220	BDL	1.74	0.010	1.10	82	9	0.19
184.	River Orsang at Chotta Udaipur	8.02	7.34	1.00	8.00	300	BDL	1.74	0.010	1.05	11	2	0.81
185.	River Orsang at Orsang Bridge Bodeli, Chhottaudaepur	7.92	7.27	1.00	6.00	312	BDL	5.10	BDL	4.00	11	2	0.98
186.	River Vishwamitri at Convent School, Fatehgunj, Vadodara	7.40	1.86	3.00	22.00	486	2.10	3.16	0.120	0.80	>1600	>1600	0.70
187.	River Vishwamitri at Kamatibaug- Sayajibaug, Vadodara	7.38	1.63	3.00	20.00	506	3.18	4.28	0.010	0.78	>1600	>1600	0.63
188.	River Vishwamitri near Gujarat Tractor Ltd., Munjmahuda, Vadodara	7.41	1.24	3.00	18.00	542	3.86	5.10	0.010	0.60	>1600	>1600	0.69
189.	River Vishwamitri near Kalali Rly Crossing, Vadodara	7.07	2.87	3.00	32.00	696	BDL	0.86	0.010	0.30	>1600	>1600	0.71
190.	River Damanganga at GIDC Vapi Weir	7.77	7.00	0.80	10.00	232	0.28	1.12	0.007	0.24	40	14	0.14
191.	River Damanganga at Madhuban Dam	8.21	7.10	0.60	6.00	180	0.28	1.12	0.020	0.30	<1.8	<1.8	0.20
192.	River Par Weir at Atul	8.23	7.10	0.70	10.00	240	0.28	1.12	0.032	0.14	25	6	0.28
193.	Tube well near Tower, Vasad Gram Panchayat, Anand	7.88	4.12	-	6.00	592	BDL	-	0.001	3.9	<2	<2	0.37

Sr. No.	Sampling Location/ Stations	Parameters*											
		pH	DO	BOD	COD	TDS	NH_3-N	TKN	NO_2-N	NO_3-N	TC	FC	F
194.	Tube well at Luna Gram Panchayat	7.35	4.05	1.00	8.00	478	BDL	5.10	BDL	5.46	<2	<2	0.73
195.	Tube well Karakhadi Gram panchayat, Ta. Padra, Vadodara	7.72	3.87	1.00	8.00	4,152	BDL	6.12	0.010	5.24	<2	<2	1.08
196.	Tube well Dabhasa Gram panchayat, Ta. Padra, Vadodara	7.63	3.97	1.00	8.00	1,532	BDL	5.40	BDL	3.70	<2	<2	0.86
197.	Tube well Ekalbara Gram panchayat, Wadipura, Mota Ekalbara, Vadodara	7.02	4.24	1.00	8.00	2,210	BDL	6.22	0.010	5.30	<2	<2	0.80
198.	Tube well H.J. Amin at Chhani, Vadodara	7.93	3.87	1.00	8.00	1,702	BDL	5.10	BDL	4.00	<2	<2	0.36
199.	Tube well Jaspur Gram panchayat, Ta. Padra, Vadodara	7.39	4.08	1.00	8.00	1,530	BDL	4.12	0.010	3.80	<2	<2	1.07

*Note: Except pH, TC (MNP/100 ml) & FC (MNP/100 ml), all the parameters are expressed as mg/L.

ANNEXURE - 22

Results of water monitoring carried out under the Well water monitoring project (annual average of the year 2024-25)

Sr. No.	Location of wells	Parameters*									
		pH	TDS	DO	COD	NO_2-N	NO_3-N	F	NH_3-N	TC	FC
1.	Borewell of Bareja, Ahmedabad	7.50	1,662	-	9.00	0.110	0.85	0.22	-	-	-
2.	Borewell of Dholka Nagarpalika	7.09	2,398	6.93	9.00	0.050	0.40	0.98	1.85	<2	<2
3.	Borewell of Bavla Nagarpalika	7.93	702	7.21	8.00	0.050	0.55	1.70	1.74	<2	<2
4.	Borewell of Dhandhuka Nagarpalika	7.61	1,788	7.97	7.00	0.080	0.14	1.00	1.01	<2	<2
5.	Borewell of Sanand Nagarpalika	7.63	1,306	7.93	8.00	0.050	0.37	1.93	0.92	<2	<2
6.	Borewell of Old Pungam, Bharuch	8.41	778	-	7.00	0.630	1.96	0.76	BDL	<2	<2
7.	Borewell of Shri Ahmedbhai Patel at Piraman, Ankleshwar	7.20	1,978	-	8.00	0.021	0.46	0.71	BDL	<2	<2
8.	Borewell of Khadiwala, Piraman	7.99	1,464	-	8.00	0.031	0.85	0.85	BDL	<2	<2
9.	Borewell of Gram Panchayat, Piraman	7.93	1,476	-	8.00	0.026	0.79	0.68	BDL	<2	<2
10.	Borewell of Gram Panchayat, Sarangpur	8.35	712	-	9.00	0.058	0.91	0.78	BDL	<2	<2
11.	Borewell of Gram Panchayat, Dadhal	8.38	1,614	-	5.00	0.063	0.84	0.71	BDL	<2	<2
12.	Borewell of Gram Panchayat, Kosamadi	8.43	1,478	-	7.00	0.028	1.12	0.99	BDL	<2	<2
13.	Well of Gram Panchayat, Bhadkodra	8.37	746	-	9.00	0.046	0.74	1.02	BDL	<2	<2
14.	Borewell of Jitali village	8.04	1,426	-	6.00	0.054	0.86	0.68	BDL	<2	<2
15.	Borewell of Shri Ramanbhai Panchal at Shaktinagar, Dahej, Bharuch	7.87	965	-	6.17	0.128	1.98	0.52	BDL	-	-
16.	Borewell of Udesinh Parmar at Dahej, Bharuch	7.92	1,304	-	5.83	0.148	5.50	0.65	BDL	-	-
17.	Borewell of Sadbhavna Nursery, Kalak Road, Jambusar, Bharuch	7.73	2,323	-	5.33	0.190	2.20	0.50	0.56	-	-
18.	Well of Wasmo, Village Mathawada.	7.63	1,363	-	12.00	-	-	0.35	-	<1.8	<1.8

Sr. No.	Location of wells	Parameters*									
		pH	TDS	DO	COD	NO_2-N	NO_3-N	F	NH_3-N	TC	FC
19.	Open well of Shri Rajubhai Solankis farm, Village Alang	7.58	2,307	-	9.00	-	-	0.29	-	<1.8	<1.8
20.	Open well of Shri Gobarbhai Solanki farm, Village Alang	7.61	1,510	4.30	6.50	-	-	0.33	-	<1.8	<1.8
21.	Open well of Shri Bhagwansinh Gohil farm, Village Sosiya	7.61	1,089	4.33	7.50	-	-	0.30	-	<1.8	<1.8
22.	Open well of Shri Virjibhai Patel farm, Village Manar	7.48	1,201	4.28	7.50	-	-	0.33	-	<1.8	<1.8
23.	Well of farm of Shri Vallabhbhai Italiya, Alang	7.50	1,748	4.23	7.50	-	0.64	0.32	1.40	<1.8	<1.8
24.	Borewell of Bajarangdas Bapa Madhuli, Alang	7.57	1,904	4.30	8.00	-	0.72	0.32	1.12	<1.8	<1.8
25.	Well of farm of Shri Kalubhai Italiya, Alang	7.37	1,507	4.25	8.75	-	0.61	0.33	1.40	<1.8	<1.8
26.	Well of farm of Shri Jivabhai Patel, Alang	7.44	1,252	4.33	7.75	-	0.60	0.32	1.26	<1.8	<1.8
27.	Borewell of Chhatral Industrial Area, Gandhinagar	7.14	1,497	5.92	8.16	0.060	0.59	-	0.47	<2	<2
28.	Borewell of Chhtral Gram Panchayat, Gandhinagar	7.27	1,213	6.59	7.83	0.040	0.44	0.61	0.48	<2	<2
29.	Borewell of GPCB new building, Gandhinagar	7.71	502	7.04	6.87	0.070	0.48	1.24	0.40	<2	<2
30.	Borewell of GIDC Kalol, Gandhinagar	7.38	1,409	6.41	8.16	0.050	0.43	-	0.47	<2	<2
31.	Borewell of Palsana, Gandhinagar	7.47	2,296	6.40	7.50	-	0.84	0.70	0.35	<2	<2
32.	Borewell of Ranjitnagar Gram Panchayat, Panchmahal	6.90	988	-	9.00	0.020	12.11	0.16	BDL	<2	<2
33.	Borewell of Mandir Falia, Halol, Panchmahal	7.28	760	-	10.00	0.380	15.00	0.15	BDL	<2	<2
34.	Borewell near Bus Stand, Kalol, Panchmahal	7.00	1,282	-	8.00	0.060	18.71	0.28	BDL	<2	<2
35.	Tubewell of GWSSB, Derol, Panchmahal	7.13	1,424	-	9.00	0.036	4.92	0.11	BDL	<2	<2
36.	Borewell at Thakkarbapa Chowk, Dahod	7.06	1,324	-	7.00	0.020	5.66	0.20	BDL	<2	<2
37.	Borewell of Nava Bazar, Ghodhra, Panchmahal	7.16	488	-	8.00	0.570	13.98	0.34	BDL	<2	<2
38.	Borewell of Santrampur Nagarpalika, Mahisagar	8.33	790	-	8.00	0.010	0.32	0.52	BDL	<2	<2
39.	Borewell of Fatehpura Gram Panchayat, Dahod	7.99	202	-	7.00	0.010	0.28	0.19	BDL	<2	<2
40.	Borewell of ZalodNagarpalika, Dahod	8.02	242	-	8.00	0.010	0.32	0.19	BDL	<2	<2

Sr. No.	Location of wells	Parameters*									
		pH	TDS	DO	COD	NO_2-N	NO_3-N	F	NH_3-N	TC	FC
41.	Borewell of Zalod Road, Near Under Bridge Dahod, Dahod	7.34	558	-	9.00	0.500	5.43	0.16	BDL	<2	<2
42.	Borewell of Desai wada, Besides wanikwadi, Dahod	7.50	334	-	9.00	0.400	4.03	0.24	BDL	<2	<2
43.	Borewell near Limkheda char rasta, Dahod	7.02	726	-	8.00	0.130	4.39	0.14	BDL	<2	<2
44.	Well of Dharia Farm near Limkheda, Dahod	7.11	1,132	-	7.00	0.075	5.39	0.12	BDL	<2	<2
45.	Borewell of Limkheda Gram Panchayat, Limkheda, Dahod	7.00	774	-	12.00	0.350	4.39	0.27	BDL	<2	<2
46.	Borewell of Piplod Gram Panchayat, Piplod, Dahod	7.12	560	-	7.00	0.015	3.9	0.14	BDL	<2	<2
47.	Borewell of Jagruti Society, Halol, Panchmahal	7.09	692	-	7.00	0.019	18.00	0.12	BDL	<2	<2
48.	Borewell of Himmatnagar Nagarpalika, Himmatnagar	7.41	445	6.99	7.92	0.120	1.14	1.20	0.71	<2	<2
49.	Borewell of Modasa Nagarpalika, Modasa	7.18	667	6.64	7.67	0.630	0.13	0.47	0.63	<2	<2
50.	Borewell of Shamlaji Dharmashala, Shamlaji	7.06	632	5.82	7.42	0.110	1.02	0.45	0.84	<2	<2
51.	Borewell of Rameshwarnagar Residencial Area	7.36	533	4.10	6.00	0.010	0.29	0.20	0.56	<1.8	<1.8
52.	Borewell of GIDC Office, Shanker Tekari	7.28	1,768	3.40	7.00	0.010	0.29	0.21	0.56	<1.8	<1.8
53.	Borewell of Mahavir Metallurgical, Dared GIDC, Phase 3.	7.05	1,722	4.10	6.00	0.010	0.30	0.22	0.56	<1.8	<1.8
54.	Borewell of Shri Hitendrabhai Ker, Shivshakti park, New Samshan road, Gandhinagar, Jamnagar	7.53	1,262	4.00	7.00	0.010	0.29	0.20	0.56	<1.8	<1.8
55.	Borewell of Kankeshwar Mahadev Temple, Vibhapar, Jamnagar	7.24	2,613	4.00	12.00	0.010	0.29	0.22	0.56	<1.8	<1.8
56.	Borewell of GPCB Junagadh office	7.55	804	3.90	9.56	0.022	1.38	0.28	0.28	<1.8	<1.8
57.	Borewell of GIDC Veraval	7.55	7,940	3.80	9.56	0.022	1.38	0.66	0.28	<1.8	<1.8
58.	Borewell of GIDC-II, Dolatpar, Junagadh	7.44	1,708	3.90	9.16	0.022	1.43	0.97	0.28	<1.8	<1.8
59.	Borewell of ward no. 3 & 4 of Anjar Nagarpalika	7.68	709	3.23	9.25	0.030	0.14	0.34	0.56	-	-
60.	Borewell of Mundra city, Opp. B.Ed college	7.70	2,034	3.19	9.36	0.220	0.34	0.41	0.56	-	-
61.	Borewell of Village Samakhiyali	7.72	2,855	3.31	10.00	0.040	0.14	1.08	0.56	-	-
62.	Borewell of Village Lunava, near Chopadava	7.69	903	3.14	9.83	0.030	0.29	0.25	0.56	-	-

Sr. No.	Location of wells	Parameters*									
		pH	TDS	DO	COD	NO_2-N	NO_3-N	F	NH_3-N	TC	FC
63.	Borewell of TSDF Site (D/S), Juna Katariya, Bhachau	7.86	464	3.15	8.00	-	0.14	-	0.56	<1.8	<1.8
64.	Tappar Dam at Tappar village, Tal Anjar	8.00	631	5.66	9.50	-	0.15	-	0.56	<1.8	<1.8
65.	Borewell of Kadi Industrial Area	7.61	1,055	6.71	8.50	0.081	0.66	0.58	0.28	<2	<2
66.	Borewell of GIDC Mehsana	7.97	777	5.80	7.50	0.125	0.89	0.22	0.28	<2	<2
67.	Borewell of Hanumandhara Temple, Lalpar, Morbi	7.45	2,229	3.83	8.48	0.020	1.30	0.86	0.33	-	-
68.	Borewell of Matrix Industries, Rafaleshwar GIDC, Rafaleshwar, Morbi	7.67	1,192	3.80	9.98	0.020	1.34	0.09	0.56	-	-
69.	Borewell of Atul Pharmaceutical, Wanakner GIDC, Wanakner, Morbi	7.26	1,924	3.70	9.18	0.020	1.40	0.36	1.12	-	-
70.	Borewell of Halvad GIDC, Halvad, Morbi	7.28	3,092	3.70	9.58	0.017	0.22	0.28	1.12	-	-
71.	Borewell of Mumtaz theatre, Mehmadabad, Kheda	6.73	1,128	2.45	8.00	0.020	0.73	0.60	BDL	<2	<2
72.	Borewell of Sevalia, Kheda	7.08	1,556	5.77	8.00	0.010	1.36	0.88	BDL	<2	<2
73.	Borewell of Pali Village, Kheda	6.96	3,896	7.03	7.00	0.010	1.46	0.84	BDL	<2	<2
74.	Borewell of Thasara Water Works, Kheda	7.38	666	4.24	7.00	0.020	0.28	0.98	BDL	<2	<2
75.	Borewell of Dakor Municipal Borough, Dakor, Kheda	7.18	786	5.88	7.00	0.740	0.98	0.55	0.14	<2	<2
76.	Borewell of Kapadvanj Nagarpalika, water works, Kheda	7.15	808	3.43	12.00	0.010	1.69	0.21	BDL	<2	<2
77.	Borewell of Danadara, Ta, Kapadvanj, Kheda	7.23	1,032	5.84	19.00	0.010	8.80	0.34	BDL	<2	<2
78.	Borewell of Uttarsanda, Ta. Nadiad, Kheda	7.16	784	5.88	11.00	0.002	1.94	0.90	0.39	<2	<2
79.	Borewell of Dumral, Ta. Nadiad, Kheda	7.60	1,040	6.04	11.00	0.010	1.51	0.69	0.56	<2	<2
80.	Borewell of Mehmadabad Water Works, Kheda	7.54	744	7.35	8.00	0.010	0.26	1.07	0.16	<2	<2
81.	Borewell of Mafatlal Industries, Nadiad, Kheda	8.33	1,194	6.94	9.00	0.004	2.65	0.24	BDL	<2	<2
82.	Borewell of Ramji Mandir at Chaklasi, Nadiad, Kheda	7.13	776	5.94	10.00	0.010	1.72	0.76	0.45	<2	<2
83.	Borewell of Indiranagar, Kheda	7.20	2,066	4.43	8.00	0.320	0.98	1.17	0.62	<2	<2
84.	Borewell of Palanpur Nagarpalika	7.25	1,003	7.21	7.60	0.088	0.72	0.41	-	<2	<2

Sr. No.	Location of wells	Parameters*									
		pH	TDS	DO	COD	NO_2-N	NO_3-N	F	NH_3-N	TC	FC
85.	Borewell of Patan Nagarpalika	7.49	1,402	6.68	7.90	0.106	0.90	1.14	-	<2	<2
86.	Borewell of Siddhapur Nagarpalika	7.56	831	7.01	8.00	0.070	0.79	0.93	-	<2	<2
87.	Borewell of Ambaji Nagarpalika	7.43	609	6.92	8.00	0.070	0.72	0.88	-	<2	<2
88.	Bore well of Porbandar Nagarpalika, Porbandar	7.50	1,738	3.58	6.83	0.008	0.26	0.21	0.61	-	-
89.	Well of Orient Abrasives Ltd, GIDC Dharampur, Porbandar	7.60	1,850	3.67	7.42	0.009	0.30	0.21	0.56	<1.8	<1.8
90.	Borewell at Neelam Fiber Kim Ind area	8.36	2,176	4.10	14.00	0.047	0.12	0.22	0.56	<2	<2
91.	Borewell at Piramal Glass Tarsadi at Kosamba	7.64	1,106	4.40	10.00	BDL	0.09	0.15	-	<2	<2
92.	Borewell of Pandesara Industrial area at SGTPA Hall, Surat	8.18	3,274	3.00	14.00	0.102	0.14	0.29	1.40	<2	<2
93.	Borewell at PHC Kadodara	8.47	1,006	4.20	10.00	0.076	0.12	0.19	0.28	<2	<2
94.	Borewell at SIEL, GIDC Sachin	7.78	3,072	3.20	16.00	0.100	0.18	0.25	0.56	<2	<2
95.	Borewell at Baleshwar Ind. Area (Lucky filling stn)	8.48	664	4.40	11.00	0.103	0.17	0.25	0.56	<2	<2
96.	Borewell at Gargtex-o Feb Pvt.Ltd, Olpad	7.61	9,972	6.70	24.00	0.058	0.11	0.34	0.56	<2	<2
97.	Borewell of K.B. Industry, GIDC Limbdi	7.72	10,520	3.80	9.98	0.010	1.40	2.00	0.28	<1.8	<1.8
98.	Borewell of Greenply Industries, GIDC Bamanbore	7.29	3,160	3.80	8.79	0.010	1.40	1.03	0.28	<1.8	<1.8
99.	Borewell of Madhav Complex, Sayla	7.26	1,400	3.70	7.58	0.010	1.40	0.18	0.30	<1.8	<1.8
100.	Well at Nr. Ramji temple, Chiri	7.44	750	-	8.00	0.008	0.24	0.30	-	-	-
101.	Well of Shri Bhikhabhai Mango, Chandor	7.37	268	-	8.00	0.002	0.29	0.25	-	-	-
102.	Borewell of Shri Nagarbhai Patel wadi at Namdha	7.21	206	-	8.00	0.006	0.22	0.22	-	-	-
103.	Open well at Ahwa	7.79	550	-	9.00	BDL	0.30	0.28	-	-	-
104.	Open well at Botanical Garden, Waghai	7.65	144	-	6.00	BDL	0.32	0.20	-	-	-

*Note: Except pH, TC (MNP/100 ml) & FC (MNP/100 ml), all the parameters are expressed as mg/L.

ANNEXURE - 23

Results of water monitoring carried out under the Major cities water monitoring project (annual average of the year 2024-25)

Sr. No.	Sampling Location/ Stations	Parameters*						
		pH	DO	COD	TDS	NO_2-N	NO_3-N	F
1.	Borewell of Gayatri Flat, Nr P.T College, Paldi	7.66	6.55	7.92	383	0.060	0.52	0.51
2.	Borewell of Gandhi Ashram	7.78	6.74	7.75	840	0.060	0.56	1.21
3.	Borewell of GIDC Naroda	7.50	-	9.75	927	0.092	0.60	0.63
4.	Borewell of GIDC Vatva, Phase I	7.49	-	9.67	1,257	0.064	0.61	-
5.	Borewell of Dholka Nagarpalika	7.09	6.93	9.00	2,398	0.050	0.40	0.98
6.	Borewell of Bavla Nagarpalika	7.93	7.21	8.00	702	0.050	0.55	1.70
7.	Borewell of Sanand Nagarpalika	7.63	7.93	8.00	1,306	0.050	0.37	1.93
8.	Borewell of Dhandhuka Nagarpalika	7.61	7.97	7.00	1,788	0.080	0.14	1.00
9.	Borewell of Changodar Gram Panchayat	7.22	5.84	8.00	2,233	0.082	0.60	0.79
10.	Borewell of V.U. Nagar GIDC, Water tank, Anand	7.94	4.87	7.75	1,089	0.010	4.63	0.74
11.	Borewell of Cambay Organic P. Ltd Sokhada, Ta. Khambhat.	7.91	3.97	8.67	6,029	0.020	7.91	0.81
12.	Borewell of Anand Nagarpalika, Water tank, Anand	7.72	4.35	7.83	877	0.010	1.34	0.72
13.	Borewell of Alunj Village, Ta. Ankleshwar	7.60	-	5.75	2,130	-	2.74	0.51
14.	Borewell of Industrial Carbon, Rajpipla road, Ankleshwar	7.45	-	5.00	3,932	0.024	0.87	0.42
15.	Borewell of Kararvell village	7.69	-	5.58	1,148	-	2.89	0.41
16.	Borewell of Shri Yakubbhau Chasmawala, Umarwada	7.94	-	5.60	1,748	-	2.98	0.64
17.	Borewell of Jhaghadia Grampanchayat, Jhaghadia	7.33	-	5.83	1,627	-	3.48	0.48
18.	Borewell of Shri Ramanbhai Panchal at Shaktinagar, Dahej, Bharuch	7.87	-	6.17	965	0.130	1.98	0.52
19.	Borewell of Udesinh Parmar at Dahej, Bharuch	7.92	-	5.83	1,304	0.150	5.50	0.65
20.	Borewell of Sadbhavna Nursery, Kalak Road, Jambusar, Bharuch	7.73	-	5.33	2,323	0.190	2.20	0.50
21.	Borewell of Das Pendawala Pvt. Ltd, GIDC, Chitra, Bhavnagar	7.40	4.13	6.83	904	0.044	0.69	0.32
22.	Borewell of High-Tech Investment Casting Ltd, GIDC – II, Shihor, Bhavnagar	7.50	4.33	6.92	1,016	0.042	0.89	2.66
23.	Borewell of GIDC Chhatral, Gandhinagar	7.40	6.70	7.90	1,461	0.050	0.53	0.66
24.	Borewell of Hindu Dharmshala, Dahod	7.89	5.85	8.66	577	0.020	1.84	0.74
25.	Borewell of Safari Industries, GIDC Halol	7.60	4.58	7.83	2,019	0.010	4.37	0.79

ANNEXURE - 23

Sr. No.	Sampling Location/ Stations	Parameters*						
		pH	DO	COD	TDS	NO_2-N	NO_3-N	F
26.	Borewell of Himmatnagar Nagarpalika, Sabarkantha	7.41	6.84	7.50	466	0.090	0.75	0.61
27.	Borewell of Modasa Nagarpalika, Arvalli	7.33	7.36	7.00	752	0.090	0.67	0.76
28.	Borewell of Idar Nagarpalika, Idar	7.08	5.90	8.00	838	0.070	0.55	1.15
29.	Borewell of Police Ground	7.51	3.50	7.00	1,115	0.010	0.27	0.32
30.	Borewell of GIDC Dared	7.35	3.40	8.00	1,473	0.030	0.29	0.27
31.	Borewell of Motikhavdi Gram Panchayat	7.38	4.00	7.00	1,454	0.020	0.24	0.26
32.	Borewell of Dwarka Nagarpalika	7.32	3.60	7.00	2,334	0.010	0.27	0.25
33.	Borewell of Shankar Tekri	7.60	3.30	7.00	1,273	0.010	0.29	0.22
34.	Borewell of Rameshwarnagar	7.26	4.00	6.00	831	0.010	0.24	0.22
35.	Borewell of P.K.Patel, Jetpur, Rajkot	7.41	-	8.40	727	0.017	1.32	0.19
36.	Borewell of Saubhagya Hotel, Virpur, Rajkot	7.52	-	9.33	1,122	0.018	1.35	0.34
37.	Borewell of Gangama Amar Ashram, Chowki	7.45	3.90	8.92	1,260	0.018	1.34	0.33
38.	Borewell of Bhuj city, Oppo. Old GPCB office, Bhuj	7.72	3.12	9.90	495	0.110	0.14	0.47
39.	Borewell of Kadi Industrial area	7.61	6.71	8.50	1,055	0.081	0.66	0.58
40.	Borewell of Mehsana	7.97	5.80	7.50	777	0.125	0.89	0.22
41.	Borewell of Hanumandhara Temple, Lalpar, Morbi	7.45	3.83	8.48	2,229	0.020	1.30	0.86
42.	Borewell of Nadiad Santram Mandir	7.83	-	8.00	1,285	0.020	4.86	0.71
43.	Borewell of Nadiad GIDC water Works	7.95	-	8.00	1,751	0.150	4.52	0.70
44.	Borewell of GPCB Rajkot office	7.81	3.90	7.95	644	0.016	1.23	0.29
45.	Borewell at costal highway Charrasta, Fansa, Valsad	7.50	-	9.00	502	0.020	0.32	0.30
46.	Borewell at Koliwad, Maroli, Valsad	7.87	-	9.00	778	0.020	0.31	0.31
47.	Borewell of Grampanchayat Sarigam, Sarigam, Valsad	7.48	-	12.00	578	0.010	0.36	0.34
48.	Borewell of Navinagari vasahat, at Tadgam, Valsad	8.00	-	9.00	1,452	0.010	0.32	0.38
49.	Borewell of Chandan steel Ltd (Unit-4), Umbergaon, Valsad	7.35	-	9.00	2,210	0.010	0.32	0.38
50.	Borewell No. 3 Plastichemix, Nandesari, Vadodara	7.34	4.07	56.00	3,608	0.470	5.96	0.79
51.	Borewell of Gorwa, Bhailalbhai Amin's General Hospital, Vadodara	8.03	4.68	7.00	772	0.010	1.54	0.67
52.	Borewell of Munj Mahuda nr. Hanuman Temple, Vadodara	8.00	4.32	7.00	406	0.010	0.65	0.73
53.	Borewell of Koteshwar Mahadev Temple	7.77	5.45	8.00	508	0.020	0.33	0.33
54.	Borewell of Rajasthan Bhavan Opp Sammer Appt.	7.91	5.46	8.58	458	0.020	0.34	0.32

Sr. No.	Sampling Location/ Stations	Parameters*						
		pH	DO	COD	TDS	NO_2-N	NO_3-N	F
55.	Borewell of Demosha Chemicals, Nr Kolai Khadi, GIDC Gundlav	7.99	5.45	9.42	1,158	0.010	0.29	0.35
56.	Tokarkhadi at Khatalwada	7.89	6.95	13.00	512	-	-	-
57.	Machchu Dam III, Nr. Dharampur-Timbadi road, Morbi	7.50	6.49	14.29	649	0.030	0.32	-
58.	Aji Dam II, Rajkot	7.69	6.18	20.48	720	0.031	0.24	0.38
59.	Nyari Dam I, Rajkot	8.12	6.69	8.51	340	0.031	0.22	0.30
60.	Hand pump of Haluriya Chowk, Bhavnagar.	7.52	4.28	5.67	551	0.045	0.61	0.30
61.	Hand pump at Pitanpara, Opp. Nagarpalika, Amreli	7.53	4.25	6.50	519	0.046	0.77	0.46
62.	Hand pump of Koteshwar Temple, Jafrabad road, Rajula, Amreli	7.55	4.23	7.33	651	0.048	0.77	0.43
63.	Hand pump at Kuberbaug, Mahuva, Bhavnagar	7.57	4.22	6.83	731	0.045	0.76	0.74
64.	Hand pump Nr. Star Radiator, GIDC Dahod	7.38	4.12	8.00	868	0.080	4.86	0.64
65.	Hand Pump Nr. Ashok Bakery, Opp. Railway Station, Junagadh	7.46	3.90	9.02	732	0.019	1.34	0.25
66.	Hand Pump Nr. Panchnath Mahadev Temple, Nr. College Chowk, Gondal, Rajkot	7.97	3.83	8.19	616	0.023	1.31	0.38
67.	Hand pump at Datardargah, Nr. Tokarkhadi, Khatalwada, Valsad	7.68	-	8.00	966	0.100	0.31	0.38
68.	Lake of Naroda Gram Panchayat	7.31	1.79	62.40	401	0.088	0.57	0.44
69.	Khodiyar Lake, Rajpara, Shihor, Bhavanagar	7.61	4.24	13.00	297	0.046	0.71	0.35
70.	Ranmal Talav (Lakhota talav)	7.58	4.80	12.00	364	0.010	0.24	0.22
71.	Gomti Lake Dakor	7.60	5.43	15.00	288	0.020	0.42	-
72.	Ramsagar Talav at Tarsali, Vadodara	7.86	6.29	21.00	410	0.120	0.84	-
73.	Open well of Top – 3 Park, Talaja Jakatnaka, Bhavnagar	7.56	4.37	10.08	1,135	0.043	0.83	0.37
74.	Umarwada village pond, Ankleshwar, Bharuch	8.22	7.56	5.33	282	-	0.71	0.31
75.	River Sabarmati at Narayan Ghat	7.67	5.58	20.90	226	0.070	0.63	0.47
76.	River Khari at Geratpur	7.16	0.59	104.00	1,017	0.093	0.86	0.69
77.	River Kaveri at Village Gumandev	8.17	7.65	5.41	501	-	0.95	-
78.	River Amravati, Nr. Railway track village Dadhal	8.06	7.53	6.10	556	0.120	1.16	0.41
79.	River Bhukhi (U/S) GIDC Vilayat, Bharuch	7.86	6.73	8.42	618	-	0.75	0.42
80.	River Bhukhi (D/S) GIDC Vilayat, Bharuch	7.89	6.62	9.33	749	-	0.74	0.66
81.	River Bhukhi at Damania Nallah, Jambusar Road, Bharuch	7.67	4.08	56.92	1,514	-	-	-
82.	River Dhadhar at Amod, Bharuch	7.74	5.76	16.83	504	0.930	1.54	-

ANNEXURE - 23

Sr. No.	Sampling Location/ Stations	Parameters*						
		pH	DO	COD	TDS	NO_2-N	NO_3-N	F
83.	River Kalindri Near Rajmoti Ind. (D/S), Old Ghutu Road , Ghutu, Morbi	7.63	6.23	14.21	830	0.030	0.29	0.78
84.	River Kalindri Near Mega Ceramic (M/S), Old Ghutu Road, Ghutu, Morbi	7.56	6.54	16.46	871	0.030	0.29	0.82
85.	River Kalindri Behind Neha Ceramic, Old Ghutu Road, Ghutu, Morbi	7.70	6.13	18.36	1,175	0.030	0.27	1.05
86.	River Vishwamitri at Vadsar Bridge, near Kalali Rly Crossing, Vadodara	7.72	2.67	39.00	604	0.030	0.54	-
87.	River Dhadhar at Kothwada, Padra, Vadodara	7.79	2.95	35.00	548	0.020	1.34	-
88.	River Kolak At Koteshwar Mahadev Temple Vattar Vapi	7.73	6.95	13.58	546	0.020	0.33	0.30
89.	River Damanganga At Railway Bridge Vapi	7.71	5.83	34.08	1,652	0.020	0.32	0.43
90.	Well of Shri Thakorbhai Chhaganbhai, Sarangpur	7.51	-	6.80	2,394	-	1.94	0.77
91.	Well of PMS Inds. Federation Hall, Godhra	7.39	4.83	8.08	686	0.010	2.43	0.72
92.	Well of Shri Gandabhai Vala, Opp. Somanath Academy, Kodinar	7.56	4.20	9.45	526	0.017	1.22	0.29

*Note: Except pH, all the parameters are expressed as mg/L.

ANNEXURE - 24

Results of water monitoring carried out under the Bio monitoring of water bodies project for the year 2024-25

Sr. No.	Sampling Location/ Stations	Month-Year	Range of Saprobic Score	Biological Water Quality Class	Expected level of Biodegradable Organic Matter (BOM) & DO
1.	River Sabarmati at Hansol Bridge	Apr-24	6.1	Good	Low BOM/High DO
2.	River Sabarmati at Miroli Pumping Station	May-24	5.8	Good	Low BOM/High DO
		Nov-24	5.4	Good	Low BOM/High DO
3.	Lake Nalsarovar	May-24	4.5	Moderate	Moderate BOM /DO
		Nov-24	6	Good	Low BOM/High DO
4.	River Mahi at Vasad	Apr-24	6	Good	Low BOM/High DO
		Oct-24	6	Good	Low BOM/High DO
		Jan-25	6.3	Good	Low BOM/High DO
5.	River Narmada Juna Borbhtha Bet	Apr-24	5.25	Good	Low BOM/High DO
		Oct-24	5	Good	Low BOM/High DO
		Jan-25	6	Good	Low BOM/High DO
6.	River Narmada at Dubadub Bridge, Garudeshwar	Apr-24	6.62	Good	Low BOM/High DO
		Oct-24	6.8	Good	Low BOM/High DO
		Jan-25	6.8	Good	Low BOM/High DO
7.	River Narmada at Kabirwad	Apr-24	5.5	Good	Low BOM/High DO
		Oct-24	5.4	Good	Low BOM/High DO
8.	River Mahi at Virpur	Apr-24	7.42	Very Good	Very low BOM/High DO
		Oct-24	7.07	Very Good	Very low BOM/High DO
9.	River Mahi at Anandpuri	Apr-24	7.47	Very Good	Very low BOM/High DO
		Oct-24	7.16	Very Good	Very low BOM/High DO
10.	River Mahi at Kadana Dam (D/S)	Apr-24	7.53	Very Good	Very low BOM/High DO
		Oct-24	7.32	Very Good	Very low BOM/High DO
11.	River Anas at Khusalgadh	Apr-24	7.4	Very Good	Very low BOM/High DO
		Oct-24	7.13	Very Good	Very low BOM/High DO
12.	River Panam at Lunawada	Apr-24	7.26	Very Good	Very low BOM/High DO
		Oct-24	7.12	Very Good	Very low BOM/High DO

ANNEXURE - 24

Sr. No.	Sampling Location/ Stations	Month-Year	Range of Saprobic Score	Biological Water Quality Class	Expected level of Biodegradable Organic Matter (BOM) & DO
13.	Khijadiya part-1	Aug-24	7.27	Very Good	Very low BOM/High DO
		Jan-25	7.44	Very Good	Very low BOM/High DO
14.	Khijadiya part-2	Aug-24	7.39	Very Good	Very low BOM/High DO
		Jan-25	7.56	Very Good	Very low BOM/High DO
15.	Thol Tank, Mehsana	Apr-24	6.3	Good	Low BOM/High DO
16.	River Mahi at Sevaliya	Apr-24	7	Very Good	Very low BOM/High DO
		Oct-24	6	Good	Low BOM/High DO
17.	River Tapi at Sherulla	Apr-24	7.71	Very Good	Very low BOM/High DO
		Jul-24	7.43	Very Good	Very low BOM/High DO
		Oct-24	7.27	Very Good	Very low BOM/High DO
18.	Dudhiya Talav at Navsari	Apr-24	6.4	Good	Low BOM/High DO
		Oct-24	6.5	Good	Low BOM/High DO
19.	River Purna at Vankala	Apr-24	6.85	Good	Low BOM/High DO
		Jul-24	6.12	Good	Low BOM/High DO
		Oct-24	7.22	Very Good	Very low BOM/High DO
20.	River Ambika Upstram at Pathakwadi	Apr-24	6.37	Good	Low BOM/High DO
		Jul-24	6.57	Good	Low BOM/High DO
		Oct-24	6.6	Good	Low BOM/High DO
21.	River Tapi at Weir cum Cause way	Apr-24	6.14	Good	Low BOM/High DO
		Oct-24	5	Good	Low BOM/High DO
		Jan-25	6.14	Good	Low BOM/High DO
22.	River Tapi at Kathor Bridge, N.H. No 8	Apr-24	5	Good	Low BOM/High DO
		Oct-24	5.81	Good	Low BOM/High DO
		Jan-25	5.82	Good	Low BOM/High DO
23.	River Tapi at Varachha Brid ge	Apr-24	6	Good	Low BOM/High DO
		Oct-24	5.57	Good	Low BOM/High DO
		Jan-25	5.5	Good	Low BOM/High DO

Sr. No.	Sampling Location/ Stations	Month-Year	Range of Saprobic Score	Biological Water Quality Class	Expected level of Biodegradable Organic Matter (BOM) & DO
24.	River Masma khadi at Olpad-Saras Road	Apr-24	4.9	Moderate	Moderate BOM /DO
		Oct-24	4.83	Moderate	Moderate BOM /DO
		Jan-25	6	Good	Low BOM/High DO
25.	River Tapi Nr. KAPP Bridge (D/S of Kakarapar Dam)	Apr-24	5.75	Good	Low BOM/High DO
		Oct-24	4.91	Moderate	Moderate BOM /DO
		Jan-25	6.13	Good	Low BOM/High DO
26.	Olpad Village Pond at Olpad (Lalva Talav)	Apr-24	4.8	Moderate	Moderate BOM /DO
		Oct-24	6.13	Good	Low BOM/High DO
		Jan-25	6.4	Good	Low BOM/High DO
27.	Baleshwar Khadi on N.H no 8	Apr-24	6.14	Good	Low BOM/High DO
		Oct-24	5.5	Good	Low BOM/High DO
		Jan-25	5.57	Good	Low BOM/High DO
28.	River Tapi at Mandvi bridge	Apr-24	5.43	Good	Low BOM/High DO
		Oct-24	5	Good	Low BOM/High DO
		Jan-25	6	Good	Low BOM/High DO
29.	River Damanganga at GIDC Weir-Vapi	Apr-24	6.4	Good	Low BOM/High DO
		Oct-24	6.5	Good	Low BOM/High DO
30.	River Damanganga at Zari Causeway	Apr-24	3.7	Moderate	Moderate BOM /DO
		Oct-24	4	Moderate	Moderate BOM /DO
31.	River Kolak at Patalia Bridge	Apr-24	4.8	Moderate	Moderate BOM /DO
		Oct-24	5.67	Good	Low BOM/High DO

ANNEXURE - 25

Results of water monitoring carried out under the Coastal water monitoring project (annual average of the year 2024-25)

Sr. No.	Sampling Location/ Stations	Parameters *				
		pH	DO	BOD	COD	NH_3-N
1.	Coastal Water at Dhuvaran, Anand	8.06	6.50	1.64	-	0.51
2.	Estuarine water at Dhuvaran, Anand	8.06	6.13	1.93	-	0.51
3.	Coastal Water at Kavi Kamboi, Bharuch	7.89	6.84	1.02	-	BDL
4.	Coastal Water at Reliance Jetty, Bharuch	7.93	6.85	1.06	N.A. #	BDL
5.	Coastal Water at Hindalco Jetty, Bharuch	7.86	6.65	0.82	N.A. #	BDL
6.	Coastal Water at LNG-Jetty, Bharuch	7.83	7.01	1.12	N.A. #	BDL
7.	River Narmada at Golden Bridge	8.16	7.26	0.90	7.00	BDL
8.	River Narmada at Bhadbhut	8.05	7.04	0.88	8.83	BDL
9.	Excel Crop Care Ltd., Bhavnagar	7.25	3.82	30.76	129.42	9.32
10.	BMC waste water at Kansara nalla, Bhavnagar	7.08	4.00	106.37	368.23	13.58
11.	Pipavav Port, Amreli	8.05	6.56	3.92	30.77	3.02
12.	Nirma Ltd, Kalatalav, Bhavnagar	7.91	6.01	5.38	37.46	2.80
13.	Plot 6, SBY, Alang, Bhavnagar	7.95	6.44	5.45	37.54	3.14
14.	Plot 110, SBY, Sosiya, Alang, Bhavnagar	8.05	6.60	3.25	28.83	2.24
15.	JMC Domestic out fall w/w from pumping station of Gandhinagar Rly Station	7.16	1.20	69.00	194.50	11.40
16.	Coastal Water at Rozy Port, Near Light House	7.91	5.40	1.10	-	0.65
17.	Coastal Water at Sachana Ship Breaking yard	7.95	5.40	1.40	-	0.70
18.	Final outlet of Tata chemicals Mithapur (after dilution after settling)	8.07	5.40	1.30	-	0.65
19.	Coastal Water Nr. Arambhada village down stream of Tata Chemicals Ltd.	7.99	5.50	1.30	-	0.79
20.	Reliance Industries Limited (Sea water Basin Outlet)	7.85	5.40	1.30	-	0.70
21.	Coastal Water collected @ 2 kms away from RIL Jetty	7.96	5.50	1.20	-	0.74
22.	Essar Oil Limited (Sea water Basin Outlet)	8.09	5.30	1.30	-	0.70
23.	Coastal Water collected @ 2 kms away from Essar Jetty	8.03	5.40	1.20	-	0.66
24.	Cooling water returns through open channel water sample of GEB TPS, Sikka	7.92	5.30	1.40	-	0.78
25.	Coastal Water at Narara Island	8.05	5.50	1.20	-	0.70

Sr. No.	Sampling Location/ Stations	Parameters *				
		pH	DO	BOD	COD	NH_3-N
26.	Surface sea water, Mul Dwarka	7.75	5.56	2.07	40.94	0.37
27.	Surface sea water, Somnath	7.69	5.52	2.09	41.26	0.47
28.	Surface Sea Water, Holiday Camp, Chorvad	7.67	5.50	2.00	41.29	0.79
29.	Surface sea water, Veraval	7.66	5.50	2.08	43.42	0.37
30.	Surface sea water, Sutrapada	7.67	5.50	2.10	42.70	0.70
31.	Domestic Waste Water of Veraval Municipality Nr. Vasant Vihar Engg., Veraval	7.30	BDL	91.00	280.00	25.41
32.	Waste water Sample of Fish Processing Unit, GIDC, Veraval	7.32	BDL	271.00	888.00	86.76
33.	Coastal Water near Kandla Port, Kand la, Ta. Gandhidham	7.77	5.52	2.75	75.75	0.56
34.	Coastal Water of outlet of KSEZ /Gandhidham, Kidana	7.78	0.67	31.33	102.00	27.00
35.	Coastal Water collected near OPG TPP intake channel, Mundra	7.74	5.35	2.82	80.6	0.56
36.	Domestic water monitoring of outlet of KSEZ /Gandhidham, Kidana, under ICZM project	7.78	0.67	31.33	102.00	27.00
37.	Coastal Water of Kandal Port under ICZM project	7.77	5.52	2.75	75.75	0.56
38.	Coastal Water of confluence point of discharge channel of Adani & Tata TPP under ICZM project	7.79	5.29	2.81	79.73	0.56
39.	Coastal Water of at New Jetty of Mundra port under ICZM project	7.97	5.33	2.47	76.25	0.53
40.	Coastal Water of at Old Jetty of Mundra port under ICZM project	7.83	5.25	2.75	74.42	0.56
41.	Coastal Water at village Mandvi, Bandar road, Mandvi	7.89	5.36	2.90	75.00	0.56
42.	Surface sea water at Navalakhi Port, Navalakhi, Ta. Maliya, Morbi	7.68	5.51	2.08	41.89	0.51
43.	Surface sea water at Surajbari Creek, Surajbari, Ta. Maliya, Morbi	7.71	5.49	2.10	42.12	0.51
44.	Sea water at Chopati, Porbandar	8.04	5.48	1.24	-	0.65
45.	Domestic wastewater of Nagarpalika at Jubeeli bridge, Porbandar	7.25	-	45.80	140.00	9.19
46.	Sarigam Diffuser at – Tadagam, Valsad	7.84	6.56	1.80	-	0.70
47.	River Tapi at Umara Temple	7.83	6.67	1.60	-	0.84
48.	River Tapi at KRIBHCO Jetty	7.77	6.60	1.70	-	0.95
49.	River Tapi at ESSAR Jetty	7.75	6.60	1.70	-	0.86
50.	E.C.P. at 'J' Point near Sarod village	7.68	-	45.66	209.00	10.46
51.	Coastal Water at Sarod village	7.99	6.67	1.47	-	1.13
52.	Estuarine Water at Sarod village	8.05	6.66	1.48	-	1.40
53.	Estuarine water of river Damanganga at Daman Jetty	7.81	6.54	1.39	-	0.98
54.	Estuarine water of river Damanganga at Kanchigam	7.78	6.53	1.35	-	1.56
55.	Estuarine water of river Kolak at Kolak Jetty	7.77	6.63	1.36	22.92	1.21
56.	Estuarine water of river Par at Umarsadi Jetty	7.77	6.57	1.38	-	1.07

*Note: Except pH, all the parameters are expressed as mg/L.

• N.A. # : Not analysed due to high chloride interference.
